

Additional Construction Progress Photos

Utilizing hydraulic breaker for Lake Intake shaft excavation




Program Summary Schedule

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	2007 2008 2009 2010					
Contract No.1 - Intake												
A1102	Pre Construction Activities - Contract No. 1	107*	0*	100	01MAY07A	01OCT07A						
A1120	Contract No. 1 (Intake) Bid Period:	53*	0*	100	01MAY07A	16JUL07A						
A1320	Contract No. 1 - Intake	459*	300*	0	25OCT07A	25JAN09						
A1440	Intake Shaft Construction	267*	169*	0	12NOV07A	26NOV08						
A1580	Lake-Top Operations & Underwater Work	182*	125*	0	11JAN08A	25SEP08						
A1530	Microtunnel Installation	55*	55*	0	13JUN08	29AUG08						
A1760	Commissioning - Contract No. 1	82*	82*	0	29SEP08	23JAN09						
Contract No.2 - Pump Stations, Tanks, SCADA, etc												
A1155	Pre Construction Activities - Contract No. 2	64*	0*	100	02JUL07A	01OCT07A						
A1310	Contract No. 2 Bid Period	33*	0*	100	02JUL07A	16AUG07A						
A1745	Contract 2 - Pump Stations	760*	667*	0	19NOV07A	05NOV10						
A2660	Construction - Cuesta Tunnel Tank	138*	138*	0	01APR08	14OCT08						
A2410	Construction - Rocky Canyon Pump Station & Tank	297*	297*	0	01APR08	29MAY09						
A2120	Construction - Camp Roberts Tank	115*	115*	0	02JUN08	11NOV08						
A2240	Construction - Santa Ysabel Pump Station	236*	236*	0	25AUG08	28JUL09						
A1950	Construction - Intake Pump Station	194*	194*	0	01DEC08	02SEP09						
A2840	Overall System Startup Testing	53*	53*	0	29JUL09	12OCT09						
A2900	Commissioning - Contract No. 2	329*	329*	0	29JUL09	05NOV10						
Contract No.3 - Pipeline North												
A1195	Pre Construction Activities - Contract No. 3	84*	0*	100	01MAY07A	28AUG07A						
A1200	Contract No. 3 (PL North) Bid Period:	56*	0*	100	01MAY07A	19JUL07A						
A2870	Contract No. 3 - Pipeline North (Units A, A1, C,	605*	504*	0	07NOV07A	23MAR10						
A3170	Commissioning - Contract No. 3	76*	76*	0	04DEC09	23MAR10						
Contract No.4 - Pipeline Central												
A1238	Pre Construction Activities - Contract No. 4	85*	0*	100	01MAY07A	29AUG07A						
A1240	Contract No. 4 (PL Middle) Bid Period:	61*	0*	100	01MAY07A	26JUL07A						
A3250	Contract No 4 Pipeline Central (Units D, E, F)	518*	404*	4	19OCT07A	29OCT09						
A3590	Commissioning - Contract No. 4	138*	138*	0	16APR09	29OCT09						
Contract No.5 - Pipeline South												
A1278	Pre Construction Activities	85*	0*	100	01MAY07A	29AUG07A						
A1280	Contract No. 5 (PL South) Bid Period:	66*	0*	100	01MAY07A	02AUG07A						
A3560	Contract No 5 Pipeline South (Units G, G1, H)	529*	420*	0	28OCT07A	20NOV09						
A3930	Commissioning - Contract No. 5	45*	45*	0	21SEP09	20NOV09						



NWP NACIMIENTO WATER PROJECT
 San Luis Obispo County Flood Control & Water Conservation District

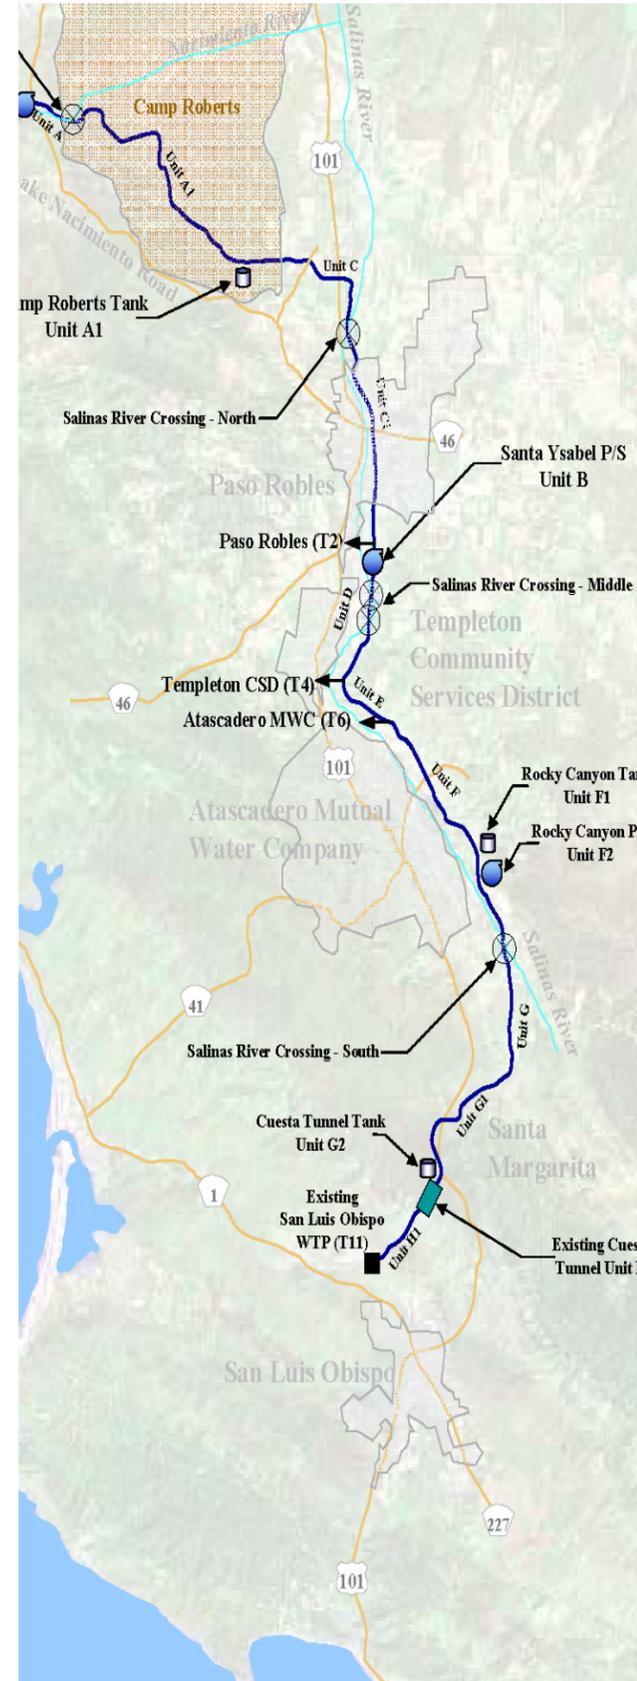

Prepared for:

John Hollenbeck
 San Luis Obispo County Flood Control & Water Conservation District
 Nacimiento Water Project
 NWP Project No. 300187.08

SUMMARY CONSTRUCTION REPORT NO. 04

Reporting Period: 3/1/08 to 3/31/08
 March 2008

- Construction – Team Effort**
 Bid Package 1 – Lake Intake
 Bid Package 2 – Facilities
 Bid Package 3 – Pipeline North
 Bid Package 4 – Pipeline Central
 Bid Package 5 – Pipeline South

Submitted by:

JACOBS
 Ed Weyrauch, Construction Manager
 3650 La Cruz Way, Suite D
 Paso Robles, CA 93446
 805 434 – 0601

Nacimiento Water Project
(Contract 300187.08)

Project Value: \$176,057,695
Designer: Black & Veatch
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Completed approximately 6,180 lf of pipeline in Rocky Canyon Road
- Completed the first 20 ft of the vertical shaft of the Lake Intake
- Completed submittals and planning to start the Pipeline – South

Work Completed This Month:

- Pipeline South began pipe laying operations on El Camino Real
- Completed third segment of vertical shaft liner for the Lake Intake
- Pipeline Central completed an additional 6,500 ft of pipe installation



Pipeline installation El Camino Real

Milestones:

System operationally tested and pumping water by December 2010

Construction Progress:

- Installed approximately 16,380 lf of pipeline through March, 12,680 lf for the central project and 3,700 lf for the south project
- Completed repaving of 13,800 lf of pipeline trench
- Completed third 12.5 ft section of Lake Intake vertical shaft
- Excavated shaft to 44 ft depth

Lake Intake
(Contract 300187.08.01)

Contract Value: \$20,816,600
Contractor: James W. Fowler Co.
Final Completion: January 25, 2009

Prior Month's Main Accomplishments:

- Completed reinforcing and block-outs for first 12.5 ft segment of shaft
- Installed forms and placed concrete for first segment of vertical shaft liner

Work Completed This Month:

- Completed two additional segments of the shaft liner, for a total of 37.5 ft
- Excavated shaft to a depth of 44 ft

Budget:

- \$1,823,000 in approved payments
- No changes issued this month



Excavation for vertical shaft inner liner

Schedule:

Contractor is reviewing his schedule, based upon progress and may need to make adjustments. Contractor has set the objective of a one week cycle for liner segments

Progress:

Work in Place - \$2,972,000
% Complete – 14.3
Time Used – 37.5%

Scheduled Budget vs. Approved Invoice:



Facilities
(Contract 300187.08.02)

Contract Value: \$25,588,000
Contractor: Mountain Cascade, Inc.
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Submittals and construction planning

Work Completed This Month:

- Submittals and construction planning for start at Rocky Canyon Pump Station and Cuesta Tank.

Budget:

- \$294,000 in approved payments
- No changes issued this month



Rocky Canyon Tank site

Schedule:

Contractor's scheduled work start has slipped to an April 8th start of excavation at Rocky Canyon PS, followed by the Cuesta Tank.

Progress:

Work in Place - \$500,000
% Complete – 2.0
Time Used – 15.3%

Scheduled Budget vs. Approved Invoice:



Pipeline North
(Contract 300187.08.03)

Contract Value: \$38,355,245
Contractor: Teichert Construction
Final Completion: March 23, 2010

Prior Month's Main Accomplishments:

- Submittals and construction planning

Work Completed This Month:

- Submittals and construction planning
- Purchased pipe for section C1

Budget:

- \$250,000 in approved payments
- No changes issued this month



Coating 30" Pipe at Northwest Pipe


Schedule:

Contractor revised the scheduled start of pot holing on Monterey Road to April, with pipe installation planned for the second week of April.

Progress:

Work in Place - \$1,175,000
% Complete – 3.1
Time Used – 20.0%

Scheduled Budget vs. Approved Invoice:



Pipeline Central
(Contract 300187.08.04)

Contract Value: \$22,879,485
Contractor: Whitaker Contractors, Inc.
Final Completion: October 29, 2009

Prior Month's Main Accomplishments:

- Continued pipe laying operations on Rocky Canyon Road, completed 6,180 ft by end of month
- Began repaving of Rocky Canyon Road

Work Completed This Month:

- Began pipe laying operations on Templeton Road, installed 6,500 ft.
- Repaved all work areas on Rocky Canyon Road

Budget:

- \$1,832,000 in approved payments
- No changes issued this month



Repaving Rocky Canyon Road


Schedule:

Contractor reached a MOA restricted area on Rocky Canyon Road and mobilized to Templeton Road heading north.

Progress:

Work in Place - \$3,100,000
% Complete – 13.7
Time Used – 22.6%

Scheduled Budget vs. Approved Invoice:



Pipeline South
(Contract 300187.08.05)

Contract Value: \$16,322,594
Contractor: Southern California Pipeline
Final Completion: November 21, 2009

Prior Month's Main Accomplishments:

- Submittals and construction planning

Work Completed This Month:

- Started pipeline installation on El Camino Real, installed 2,920 ft

Budget:

- \$108,000 in approved payments
- No changes issued this month



So Cal Pipeline on El Camion Real

Schedule:

Contractor began work on El Camino Real heading south of the Santa Margarita Creek crossing

Progress:

Work in Place - \$1,600,000
% Complete – 9.8
Time Used – 23.1%

Scheduled Budget vs. Approved Invoice:

