


Additional Construction Progress Photos

Diver Working on Lake Intake Pipe Support Columns

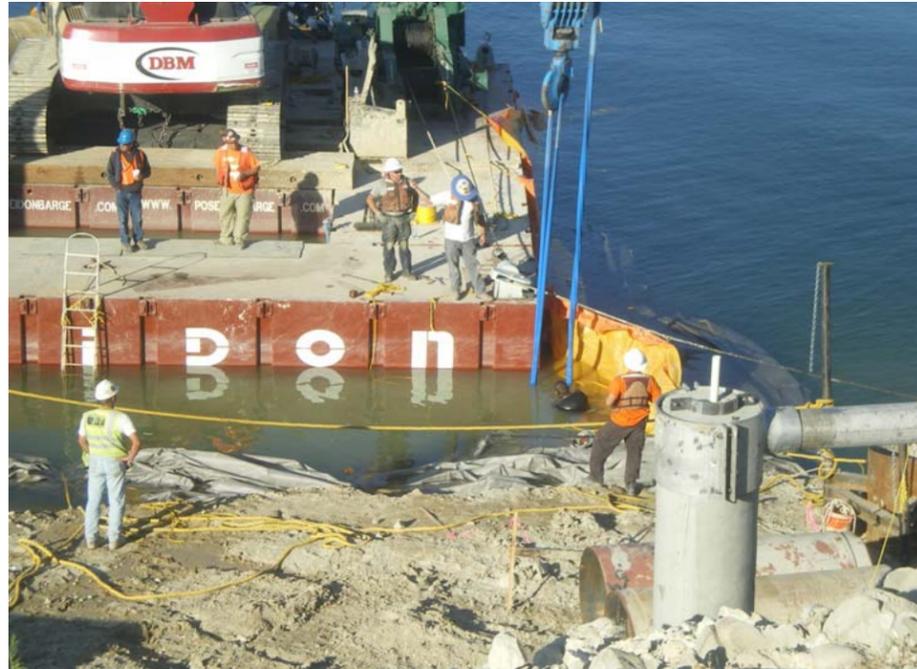


Program Summary Schedule

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	2007	2008	2009	2010
Contract No. 1 - Intake										
A1102	Pre Construction Activities - Contract No. 1	107*	0*	100	01MAY07A	01OCT07A	█			
A1120	Contract No. 1 (Intake) Bid Period:	53*	0*	100	01MAY07A	16JUL07A	█			
A1320	Contract No. 1 - Intake	484*	203*	65	25OCT07A	19FEB09		█		
A1440	Intake Shaft Construction	257*	73*	41	12NOV07A	12NOV08		█		
A1580	Lake-Top Operations & Underwater Work	874*	731*	63	11JAN08A	03JUN11		█		
A1530	Microtunnel Installation	52*	52*	0	14AUG08	27OCT08			█	
A1760	Commissioning - Contract No. 1	103*	103*	0	25SEP08	19FEB09				█
Contract No. 2 - Pump Stations, Tanks, SCADA, etc										
A1155	Pre Construction Activities - Contract No. 2	64*	0*	100	02JUL07A	01OCT07A	█			
A1310	Contract No. 2 Bid Period	33*	0*	100	02JUL07A	16AUG07A	█			
A1745	Contract 2 - Pump Stations & Tanks	628*	449*	15	19NOV07A	05MAY10		█		
A2410	Construction - Rocky Canyon Pump Station & Tank	302*	215*	15	31MAR08A	04JUN09		█		
A2660	Construction - Cuesta Tunnel Tank	189*	167*	20	01JUL08A	27MAR09		█		
A2240	Construction - Santa Ysabel Pump Station	267*	267*	0	01AUG08	18AUG09			█	
A2120	Construction - Camp Roberts Tank	199*	199*	0	11AUG08	20MAY09			█	
A1950	Construction - Intake Pump Station	202*	202*	0	15DEC08	29SEP09			█	
A2840	Overall System Startup Testing	53*	53*	0	19AUG09	02NOV09				█
A2900	Commissioning - Contract No. 2	182*	182*	0	19AUG09	05MAY10				█
Contract No. 3 - Pipeline North										
A1195	Pre Construction Activities - Contract No. 3	84*	0*	100	01MAY07A	28AUG07A	█			
A1200	Contract No. 3 (PL North) Bid Period:	56*	0*	100	01MAY07A	19JUL07A	█			
A2870	Contract No. 3 - Pipeline North (Units A, A1, C)	605*	418*	21	07NOV07A	23MAR10		█		
A3170	Commissioning - Contract No. 3	0*	0*	0	29APR10	28APR10				█
Contract No. 4 - Pipeline Central										
A1238	Pre Construction Activities - Contract No. 4	85*	0*	100	01MAY07A	29AUG07A	█			
A1240	Contract No. 4 (PL Middle) Bid Period:	61*	0*	100	01MAY07A	26JUL07A	█			
A3250	Contract No 4 Pipeline Central (Units D, E, F)	518*	318*	65	19OCT07A	29OCT09		█		
A3590	Commissioning - Contract No. 4	82*	82*	0	07JUL09	29OCT09				█
Contract No. 5 - Pipeline South										
A1278	Pre Construction Activities	85*	0*	100	01MAY07A	29AUG07A	█			
A1280	Contract No. 5 (PL South) Bid Period:	66*	0*	100	01MAY07A	02AUG07A	█			
A3560	Contract No 5 Pipeline South (Units G, G1, H)	529*	334*	45	26OCT07A	20NOV09		█		
A3930	Commissioning - Contract No. 5	206*	206*	0	03FEB09	20NOV09				█



NWP NACIMIENTO WATER PROJECT
San Luis Obispo County Flood Control & Water Conservation District

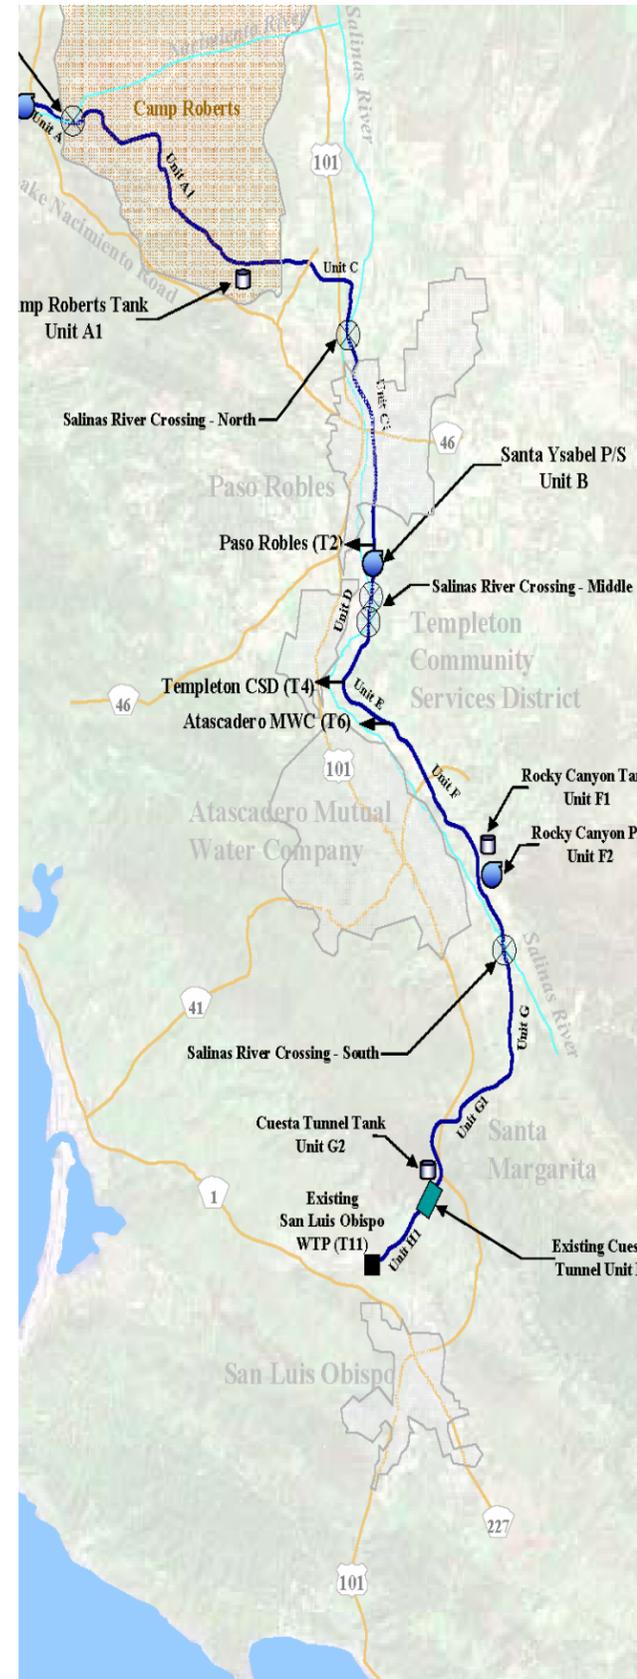

Prepared for:

John Hollenbeck
San Luis Obispo County Flood Control & Water Conservation District
Nacimiento Water Project
NWP Project No. 300187.08

SUMMARY CONSTRUCTION REPORT NO. 09

Reporting Period: 8/1/08 to 8/31/08
August 2008

- Construction – Team Effort**
 Bid Package 1 – Lake Intake
 Bid Package 2 – Facilities
 Bid Package 3 – Pipeline North
 Bid Package 4 – Pipeline Central
 Bid Package 5 – Pipeline South

Submitted by:

JACOBS
Ed Weyrauch, Construction Manager
3650 La Cruz Way, Suite D
Paso Robles, CA 93446
805 434 – 0601

Nacimiento Water Project
(Contract 300187.08)

Project Value: \$176,057,695
Designer: Black & Veatch
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Excavated shaft to depth of 161 feet
- Continued earthwork at three tank / pump station sites
- Pipe installation on Monterey Road
- Installed T2 & T6 turn-outs
- Repaved El Camino Real trench line.

Work Completed This Month:

- Completed Lake Intake vertical shaft and placed bottom slab.
- Installed intake shaft pipe supports PS-6 and PS-5.
- Excavation and re-compaction at Santa Ysabel site.
- Re-alignment of Templeton Road.
- Installed pipe through mid-river HDD.
- Installed T-4 turn-out HDD
- Repaved Sandoval Road



Drilling for Intake Pipe Supports

Milestones:

System operationally tested and pumping water by December 2010

Construction Progress:

- Installed approximately 117,968 feet of pipeline through August (16,586 feet for the North Pipeline and 63,212 feet for the Central Pipeline and 38,170 feet for the South Pipeline).
- Completed testing of 57,285 feet of pipeline.
- Completed repaving of 61,057 feet of pipeline trench.

Lake Intake
(Contract 300187.08.01)

Contract Value: \$20,822,927
Contractor: James W. Fowler Co.
Final Completion: January 25, 2009

Prior Month's Main Accomplishments:

- Eleventh segment of the shaft liner, for a total of 160 feet.
- Excavated shaft to depth of 161 feet.

Work Completed This Month:

- Completed Lake Intake vertical shaft and placed bottom slab.
- Installed intake shaft pipe supports PS-6 and PS-5.

Budget:

- \$14,672,898.00 in payment requests
- \$9,327.00 in changes through this month



Intake Shaft Base Slab Reinforcing


Schedule:

Pending resolution of the last major submittal for the hydraulic power unit, the project is expected to be on schedule. The intake tunnel work will start next month, with project substantial completion by the end of November looking feasible.

Progress:

Work in Place - \$15,713,578.00
% Complete - 75.5
Time Used - 69.4%

Scheduled Budget vs. Approved Invoice:



Facilities
(Contract 300187.08.02)

Contract Value: \$25,546,468
Contractor: Mountain Cascade, Inc.
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Continued erection of Rocky Canyon Tank.
- Began excavation and re-compaction at Santa Ysabel and Cuesta sites.

Work Completed This Month:

- Excavation and re-compaction at Santa Ysabel site.

Budget:

- \$2,355,252.00 in payment requests
- (\$41,532.00) in changes through this month



Rocky Canyon Pump Station Site Work

Schedule:

The contractor's progress at Rocky Canyon has been disrupted by problems with in place concrete strengths. Work continues at the Cuesta Tank and will start at Camp Roberts early next month. Currently contractor is behind schedule despite a planned slow start.

Progress:

Work in Place - \$3,061,799.00
% Complete - 12.0
Time Used - 28.9%

Scheduled Budget vs. Approved Invoice:



Pipeline North
(Contract 300187.08.03)

Contract Value: \$39,894,852
Contractor: Teichert Construction
Final Completion: March 23, 2010

Prior Month's Main Accomplishments:

- Pipe installation on Monterey Road, installed 3,661 feet.
- Tested 5,352 feet of installed pipe
- Repaved 5,216 feet of Monterey Road

Work Completed This Month:

- Pipe installation on Santa Ysabel and South River Roads, 2,570 feet.
- Tested 1,720 feet of installed pipe
- Repaved 6,970 feet of trenching areas

Budget:

- \$7,878,697.00 in payment requests
- \$1,539,607.00 in changes through this month



Pipe Installation- South River Road


Schedule:

Contractor is progressing with work in the more congested segments of the project. Pipe laying continued north on South River Road, but overall is slowed by coordinating pipe deliveries and gaining site access to overland areas.

Progress:

Work in Place - \$8,754,107.00
% Complete - 21.8
Time Used - 36.9%

Scheduled Budget vs. Approved Invoice:



Pipeline Central
(Contract 300187.08.04)

Contract Value: \$22,671,077
Contractor: Whitaker Contractors, Inc.
Final Completion: October 29, 2009

Prior Month's Main Accomplishments:

- Installed 12,239 feet of pipe
- Repaved 3,905 feet of trenching areas
- Testing of 11,300 feet of pipe.
- Installation of T6 and T2 turn-outs.

Work Completed This Month:

- Installed 9,243 feet of pipe
- Re-alignment of Templeton Road.
- Installed pipe through mid-river HDD.
- Installed T-4 turn-out HDD

Budget:

- \$17,730,678.00 in payment requests
- (\$26,023.00) in changes through this month



Pulling Pipe for Mid-River Crossing


Schedule:

The contractor is well ahead of schedule, 1.5 miles of mainline pipe remaining, expect to complete next month. The ties, testing and fiber optic system and appurtenance work is expected to complete by November.

Progress:

Work in Place - \$18,860,730.00
% Complete - 84.1
Time Used - 43.1%

Scheduled Budget vs. Approved Invoice:



Pipeline South
(Contract 300187.08.05)

Contract Value: \$16,869,531
Contractor: Southern California Pipeline
Final Completion: November 21, 2009

Prior Month's Main Accomplishments:

- Installed 14,157 feet of pipe
- Repaved 9,906 feet of trenching areas
- Bore & jack installations at Sandoval Road under the railroad and across highway 58.

Work Completed This Month:

- Installed 2,898 feet of pipe
- Repaved Sandoval Road
- Bore & Jack installations at Halcon Road and Yerba Buena Creek.

Budget:

- \$8,279,911.00 in payment requests
- \$536,937.00 in changes through this month



Overland Work - West Side of Hwy 101

Schedule:

Contractor is ahead of schedule but now will begin work in very difficult terrain, which may slow their productivity depending upon weather and site access.

Progress:

Work in Place - \$9,199,901.00
% Complete - 56.3
Time Used - 42.7%

Scheduled Budget vs. Approved Invoice:

