


Additional Construction Progress Photos



Clear and Grub –Rowitser Property

Program Summary Schedule

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish	2007	2008	2009	2010
Contract No.1 - Intake										
A1102	Pre Construction Activities - Contract No. 1	107"	0"	100	01MAY07A	01OCT07A				
A1120	Contract No. 1 (Intake) Bid Period:	53"	0"	100	01MAY07A	16JUL07A				
A1320	Contract No. 1 - Intake	677"	0"	95	25OCT07A	31AUG09				
A1440	Intake Shaft Construction	199"	0"	100	12NOV07A	21AUG08A				
A1530	Microtunnel Installation	32"	0"	100	02SEP08A	15OCT08A				
A1760	Commissioning - Contract No. 1	183"	0"	90	12DEC08A	31AUG09				
Contract No.2 - Pump Stations, Tanks, SCADA, etc										
A1155	Pre Construction Activities - Contract No. 2	64"	0"	100	02JUL07A	01OCT07A				
A1310	Contract No. 2 Bid Period:	33"	0"	100	02JUL07A	16AUG07A				
A1745	Contract 2 - Pump Stations & Tanks	760"	305"	70	19NOV07A	05NOV10				
A2410	Construction - Rocky Canyon Pump Station & Tank	528"	165"	80	31MAR08A	23APR10				
A2860	Construction - Cuesta Tunnel Tank	390"	92"	90	01JUL08A	12JAN10				
A2240	Construction - Santa Ysabel Pump Station	426"	136"	70	14JUL08A	15MAR10				
A2120	Construction - Camp Roberts Tank	414"	159"	60	01SEP08A	15APR10				
A1950	Construction - Intake Pump Station	366"	202"	30	12JAN08A	15JUN10				
A2900	Commissioning - Contract No. 2	169"	169"	0	16MAR10	05NOV10				
Contract No.3 - Pipeline North										
A1195	Pre Construction Activities - Contract No. 3	84"	0"	100	01MAY07A	28AUG07A				
A1200	Contract No. 3 (PL North) Bid Period:	56"	0"	100	01MAY07A	19JUL07A				
A2870	Contract No. 3 - Pipeline North (A, A1, C, C1)	605"	142"	64	07NOV07A	23MAR10				
A3170	Commissioning - Contract No. 3	49"	49"	0	14JAN10	23MAR10				
Contract No.4 - Pipeline Central										
A1238	Pre Construction Activities - Contract No. 4	85"	0"	100	01MAY07A	29AUG07A				
A1240	Contract No. 4 (PL Middle) Bid Period:	61"	0"	100	01MAY07A	26JUL07A				
A3250	Contract No 4 Pipeline Central (Units D, E, F)	491"	15"	99	19OCT07A	22SEP09				
A3590	Commissioning - Contract No. 4	35"	15"	100	04AUG09A	22SEP09				
Contract No.5 - Pipeline South										
A1278	Pre Construction Activities	85"	0"	100	01MAY07A	29AUG07A				
A1280	Contract No. 5 (PL South) Bid Period:	66"	0"	100	01MAY07A	02AUG07A				
A3560	Contract No 5 Pipeline South (Units G, G1, H)	613"	142"	90	26OCT07A	23MAR10				
A3930	Commissioning - Contract No. 5	121"	121"	0	23NOV09	23MAR10				

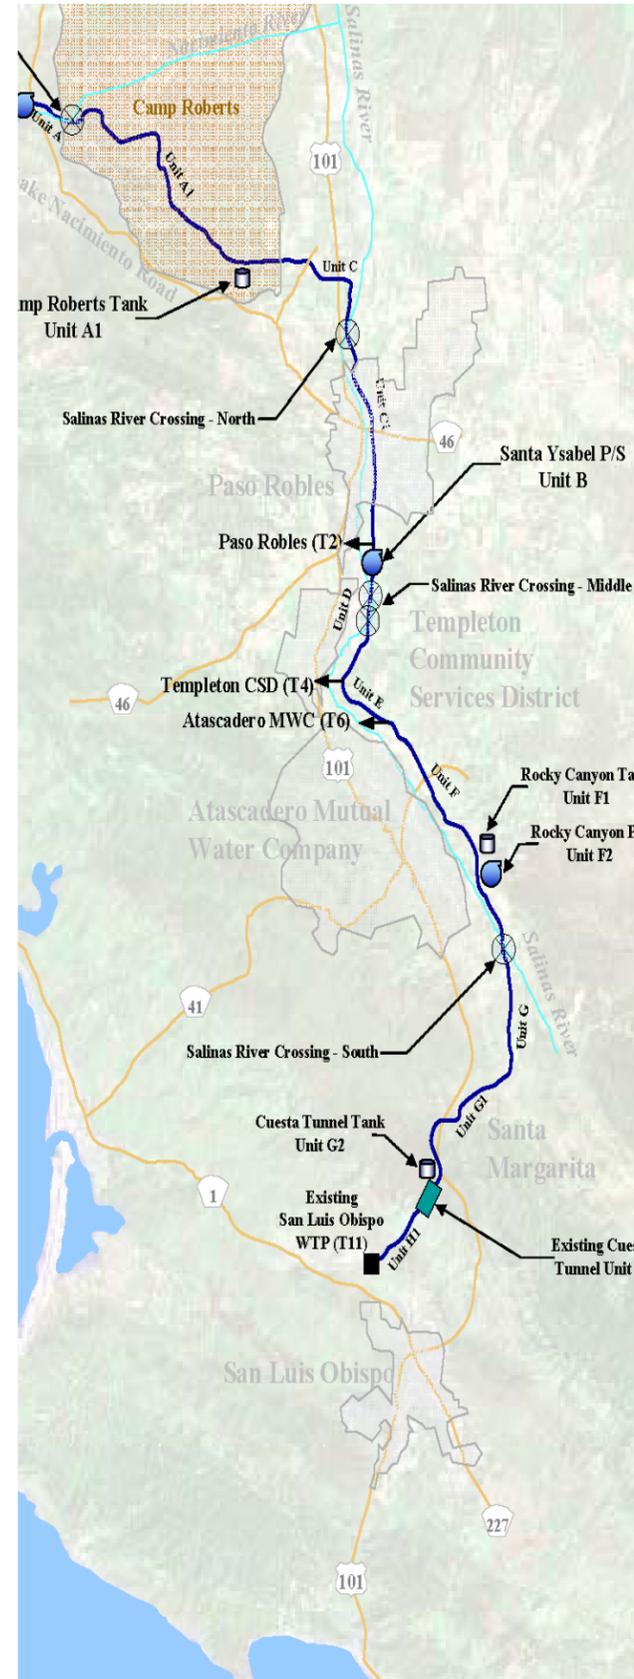

NWP NACIMIENTO WATER PROJECT
 San Luis Obispo County Flood Control & Water Conservation District

SUMMARY CONSTRUCTION REPORT NO. 21

Prepared for:

John Hollenbeck
 San Luis Obispo County Flood Control & Water Conservation District
 Nacimiento Water Project
 NWP Project No. 300187.08

Reporting Period: 8/1/09 to 8/31/09
 August 2009

- Construction – Team Effort**
- Bid Package 1 – Lake Intake
 - Bid Package 2 – Facilities
 - Bid Package 3 – Pipeline North
 - Bid Package 4 – Pipeline Central
 - Bid Package 5 – Pipeline South

Submitted by:

JACOBS

Ed Weyrauch, Construction Manager
 3650 La Cruz Way, Suite D
 Paso Robles, CA 93446
 805 434-0602

Nacimiento Water Project
(Contract 300187.08)

Project Value: \$176,057,695
Designer: Black & Veatch
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Installed 14,512 ft. of pipe.
- Completed painting Cuesta Tank
- Installed Rocky Canyon pumps and electrical gear

Work Completed This Month:

- Installed 12,958 ft. of pipe.
- Completed site grading Cuesta Tank, Camp Roberts Tank and Rocky Canyon Pump Station.
- Installed Santa Ysabel pumps and electrical gear



Pipe Installation – Camp Roberts

Milestones:

System operationally tested and pumping water by December 2010

Construction Progress:

- Installed approximately 222,403 ft. of pipeline through August (86,360 ft. for the North Pipeline and 71,123 ft. for the Central Pipeline and 64,920 ft. for the South Pipeline).
- Completed testing of 137,640 ft of pipeline.
- Completed repaving of 98,896 ft. of pipeline trench.

Lake Intake
(Contract 300187.08.01)

Contract Value: \$21,936,952
Contractor: James W. Fowler Co.
Final Completion: April 25, 2009

Prior Month's Main Accomplishments:

- None

Work Completed This Month:

- None

Budget:

- \$20,656,001 in payment requests
- \$1,123,352 in changes through this month



Lake Intake Pipe and Screens


Schedule:

Contractor plans to mobilize in September to repair the remaining actuators and will submit his final plan for repairs to the hydraulic system. Final Completion delayed pending installation of the modifications and testing.

Progress:

Work in Place - \$21,752,850
% Complete – 99.2
Time Used – 122.5%

Scheduled Budget vs. Approved Invoice:



Facilities
(Contract 300187.08.02)

Contract Value: \$25,669,315
Contractor: Mountain Cascade, Inc.
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Painting Cuesta Tank
- Installed Rocky Canyon Pumps and electrical gear

Work Completed This Month:

- Site grading of Cuesta, Camp Roberts and Rocky Canyon sites.
- Installed Santa Ysabel pumps and electrical gear

Budget:

- \$17,990,959 in payment requests
- \$81,315 in changes through this month



Installing Pump Motors – Santa Ysabel PS


Schedule:

Electrical power to Rocky Canyon Pump Station delayed to September by PG&E. Electrical and mechanical connections at Santa Ysabel PS should complete in September. Paving at Rocky Canyon Pump Station, Cuesta Tank and Camp Roberts Tank to be completed next month.

Progress:

Work in Place - \$19,190,110
% Complete – 74.8
Time Used – 61.5%

Scheduled Budget vs. Approved Invoice:



Pipeline North
(Contract 300187.08.03)

Contract Value: \$40,206,221
Contractor: Teichert Construction
Final Completion: March 23, 2010

Prior Month's Main Accomplishments:

- Installed 13,058 ft. of pipe.
- Tested 962 ft. of pipe.

Work Completed This Month:

- Installed 12,805 ft. of pipe.

Budget:

- \$30,144,401 in payment requests
- \$1,850,976 in changes through this month



Nacimiento HDD


Schedule:

Contractor will continue installing pipe on Camp Roberts and Wellsona Road and begin the San Marcos stream crossing. The Nacimiento River HDD will complete in September and will mobilize for the North Salinas HDD at the end of the month.

Progress:

Work in Place - \$33,178,282
% Complete – 82.5
Time Used – 77.4%

Scheduled Budget vs. Approved Invoice:



Pipeline Central
(Contract 300187.08.04)

Contract Value: \$22,893,031
Contractor: Whitaker Contractors, Inc.
Final Completion: October 29, 2009

Prior Month's Main Accomplishments:

- Start-up testing of turn-outs and administrative submittals.

Work Completed This Month:

- All punch-list items and equipment start-up.

Budget:

- \$21,748,379 in payment requests
- \$195,931 in changes through this month



T4 – Turn-Outs


Schedule:

The contractor is expecting final completion of all contract work by September 22, 2009.

Progress:

Work in Place - \$22,878,978
% Complete – 99.9
Time Used – 92.1%

Scheduled Budget vs. Approved Invoice:



Pipeline South
(Contract 300187.08.05)

Contract Value: \$17,821,829
Contractor: Southern California Pipeline
Final Completion: November 21, 2009

Prior Month's Main Accomplishments:

- Installed 1,454 ft. of pipe

Work Completed This Month:

- Installed 153 ft of pipe.

Budget:

- \$15,202,869 in payment requests
- \$1,489,235 in changes through this month



Placing Santa Margarita Bridge

Schedule:

The contractor will continue work south of the Cuesta Grade. The Stenner and 'Sam the Trout' crossings are expected to complete in Sept. Jack & bore under Salinas River will start in September.

Progress:

Work in Place - \$16,395,252
% Complete – 92.0
Time Used – 89.5%

Scheduled Budget vs. Approved Invoice:

