


Additional Construction Progress Photos



ARV with Valve on Wellsona Road

Program Summary Schedule

Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish
Contract No. 1- Intake						
A1102	Pre Construction Activities - Contract No. 1	107"	0"	100	01MAY07A	01OCT07A
A1120	Contract No. 1 (Intake) Bid Period:	53"	0"	100	01MAY07A	16JUL07A
A1320	Contract No. 1 - Intake	768"	0"	100	25OCT07A	30NOV09A
A1440	Intake Shaft Construction	199"	0"	100	12NOV07A	21AUG08A
A1530	Microtunnel Installation	32"	0"	100	02SEP08A	15OCT08A
A1760	Commissioning - Contract No. 1	246"	0"	100	12DEC08A	30NOV09A
Contract No. 2- Pump Stations, Tanks, SCADA, etc						
A1155	Pre Construction Activities - Contract No. 2	64"	0"	100	02JUL07A	01OCT07A
A1310	Contract No. 2 Bid Period	33"	0"	100	02JUL07A	16AUG07A
A1745	Contract 2 - Pump Stations & Tanks	760"	200"	80	19NOV07A	05NOV10
A2410	Construction - Rocky Canyon Pump Station & Tank	618"	150"	96	31MAR08A	27AUG10
A2660	Construction - Cuesta Tunnel Tank	427"	24"	96	01JUL08A	04MAR10
A2240	Construction - Santa Ysabel Pump Station	474"	79"	95	14JUL08A	20MAY10
A2120	Construction - Camp Roberts Tank	419"	59"	95	01SEP08A	22APR10
A1950	Construction - Intake Pump Station	452"	183"	80	12JAN09A	13OCT10
A2900	Commissioning - Contract No. 2	121"	121"	0	21MAY10	05NOV10
Contract No. 3- Pipeline North						
A1195	Pre Construction Activities - Contract No. 3	84"	0"	100	01MAY07A	28AUG07A
A1200	Contract No. 3 (PL North) Bid Period:	56"	0"	100	01MAY07A	19JUL07A
A2870	Contract No. 3 - Pipeline North (A, A1, C, C1)	649"	81"	95	07NOV07A	24MAY10
A3170	Commissioning - Contract No. 3	44"	44"	0	24MAR10	24MAY10
Contract No. 4- Pipeline Central						
A1238	Pre Construction Activities - Contract No. 4	85"	0"	100	01MAY07A	28AUG07A
A1240	Contract No. 4 (PL Middle) Bid Period:	61"	0"	100	01MAY07A	19JUL07A
A3250	Contract No 4 Pipeline Central (Units D, E, F)	491"	0"	100	19OCT07A	22SEP09A
A3590	Commissioning - Contract No. 4	35"	0"	100	04AUG08A	22SEP09A
Contract No. 5- Pipeline South						
A1278	Pre Construction Activities	85"	0"	100	01MAY07A	28AUG07A
A1280	Contract No. 5 (PL South) Bid Period:	66"	0"	100	01MAY07A	02AUG07A
A3560	Contract No 5 Pipeline South (Units G, G1, H)	641"	65"	93	26OCT07A	30APR10
A3930	Commissioning - Contract No. 5	90"	90"	0	01FEB10	01MAY10

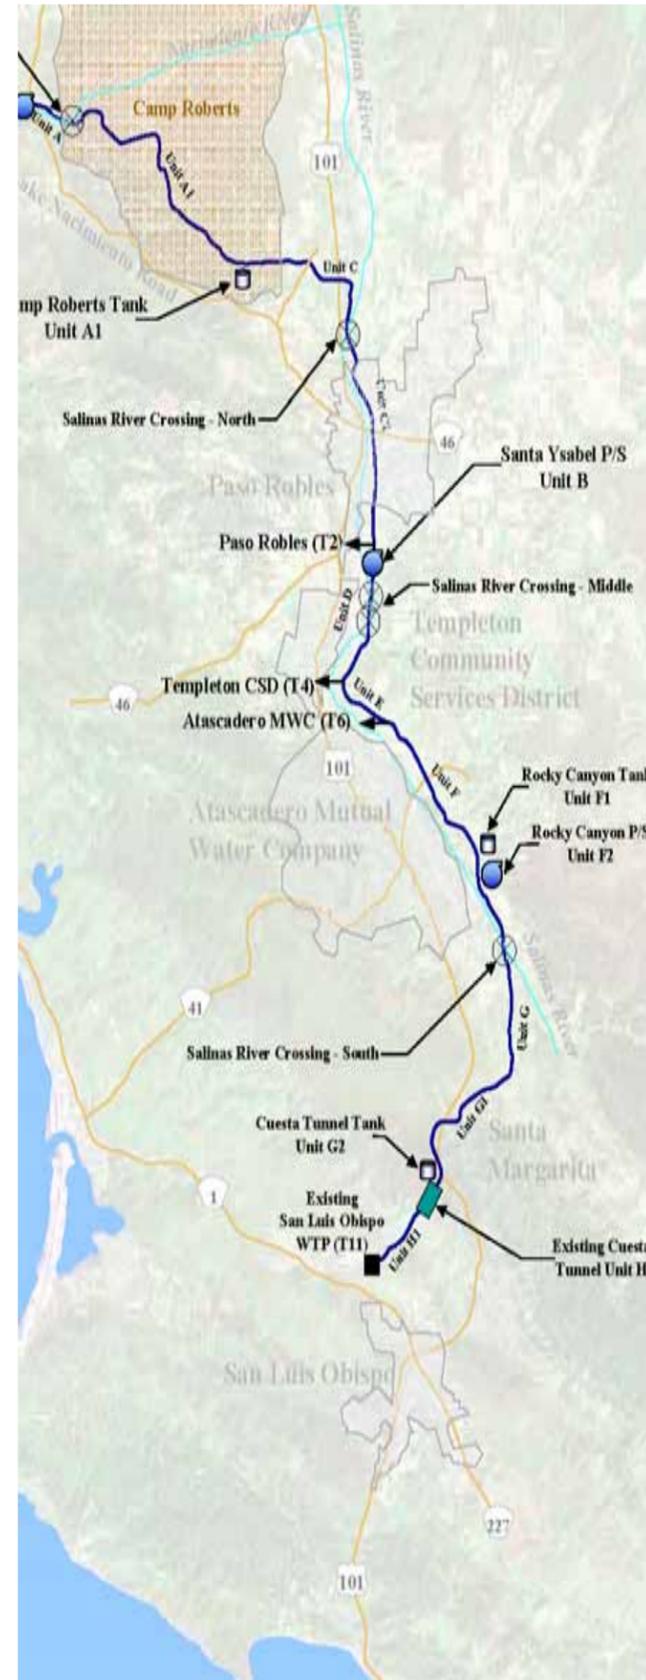

NWP NACIMIENTO WATER PROJECT
 San Luis Obispo County Flood Control & Water Conservation District

SUMMARY CONSTRUCTION REPORT NO. 26

Prepared for:

John Hollenbeck
 San Luis Obispo County Flood Control & Water Conservation District
 Nacimiento Water Project
 NWP Project No. 300187.08

Reporting Period: 1/1/10 to 1/31/10
 January 2010

- Construction – Team Effort**
 Bid Package 1 – Lake Intake
 Bid Package 2 – Facilities
 Bid Package 3 – Pipeline North
 Bid Package 4 – Pipeline Central
 Bid Package 5 – Pipeline South

Submitted by:

JACOBS

J. Overton, Construction Manager
 3650 La Cruz Way, Suite D
 Paso Robles, CA 93446
 805 434-0602

Nacimiento Water Project
(Contract 300187.08)

Project Value: \$176,057,695
Designer: Black & Veatch
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Completed pipe tie-ins at various locations.
- Tested 35,459 ft of pipe

Work Completed This Month:

- Installing ARVs, pump outs and valve boxes and testing of Fiber Optic cables for spec 3
- Installation of T-11 Vault



Santa Ysabel Pump Station

Milestones:

System operationally tested and pumping water by December 2010

Construction Progress:

- Installed approximately 255,558 ft. of pipeline through January 2010, pipeline installation essentially complete
 - North Pipeline 114,478 ft.
 - Central Pipeline 71,123 ft.
 - South Pipeline 66,657 ft.
- Completed testing of 239,060 ft. of pipeline.

Lake Intake
(Contract 300187.08.01)

Contract Value: \$21,936,952
Contractor: James W. Fowler Co.
Final Completion: April 25, 2009

Prior Month's Main Accomplishments:

- Began Negotiating Final Change Order.

Work Completed This Month:

- Continued Negotiating Final Change Order.

Budget:

- \$20,656,001 in payment requests
- \$1,123,352 in changes through this month

PROJECT COMPLETE


Schedule:

Complete Final Change Order Negotiations.

Progress:

Work in Place - \$21,752,850
% Complete – 99.2
Time Used – 85.1%

Scheduled Budget vs. Approved Invoice:



Facilities
(Contract 300187.08.02)

Contract Value: \$25,697,299
Contractor: Mountain Cascade, Inc.
Final Completion: November 5, 2010

Prior Month's Main Accomplishments:

- Continued electrical system work, SCADA system work; HVAC work, and general finishing work at IPS.
- Performed SCADA testing at Santa Ysabel, and fiber optic connections at Rocky Canyon and Santa Ysabel.

Work Completed This Month:

- Performed work at T2, T4 and T6
- Made pipe tie-in at IPS to Unit A; made pipe connections at Camp Roberts tank to Units A1 and C
- Continued general electrical, SCADA and HVAC finishing work at IPS.
- Continued SCADA testing and fiber optic work at Santa Ysabel and Camp Roberts.

Budget:

- \$21,569,406.68 in payment requests
- \$109,299 in changes through this month



Rocky Canyon Pump Station


Schedule:

Continue electrical/mechanical work at IPS; continue pre-start up activities at Rocky Canyon and Santa Ysabel.

Progress:

Work in Place - \$22,969,758
% Complete – 89.4
Time Used – 75.2%

Scheduled Budget vs. Approved Invoice:



Pipeline North
(Contract 300187.08.03)

Contract Value: \$40,517,738
Contractor: Teichert Construction
Final Completion: March 23, 2010

Prior Month's Main Accomplishments:

- Tested 35,459 ft. of pipe
- Miscellaneous work on Camp Roberts

Work Completed This Month:

- Continue testing on Wellsona Road
- Complete installation of ARV's, pump outs and valve boxes.
- Tested 19,604 ft.

Budget:

- \$36,639,293.91 in payment requests
- \$2,162,493 in changes through this month



Touchup Grading on Texas Road


Schedule:

Complete pipeline testing operations by end of January 2010.

Progress:

Work in Place - \$39,233,174
% Complete – 96.8
Time Used – 94.3%

Scheduled Budget vs. Approved Invoice:



Pipeline Central
(Contract 300187.08.04)

Contract Value: \$22,893,031
Contractor: Whitaker Contractors, Inc.
Final Completion: October 29, 2009

Prior Month's Main Accomplishments:

- Final Completion achieved 9/22/2009.

Work Completed This Month:

- Project Complete.

Budget:

- \$22,893,031 in payment requests
- \$195,931 in changes

PROJECT COMPLETE


Schedule:

Final Completion achieved on Sept 22, 2009.

Progress:

Work in Place - \$22,893,031
% Complete – 100
Time Used – 95.0%

Scheduled Budget vs. Approved Invoice:



Pipeline South
(Contract 300187.08.05)

Contract Value: \$19,153,829
Contractor: Southern California Pipeline
Final Completion: November 21, 2009

Prior Month's Main Accomplishments:

- Exposed pipe on south side of Questa Tunnel
- Began installation of pipe to T-11 and construction of vault.

Work Completed This Month:

- Completed construction of vault at T-11
- Continued installation of pipe to T-11 Turnout
- Pressure tested 4,060 LF of pipe south of Cuesta Tunnel.

Budget:

- \$16,444,040 in payment requests
- \$2,421,235 in changes through this month



Pipe Bridge

Schedule:

Continue work on T-11 Turnout and installation/testing of fiber optic cable.

Progress:

Work in Place - \$18,082,158
% Complete – 96.4
Time Used – 109.1%

Scheduled Budget vs. Approved Invoice:

