

**COUNTY OF SAN LUIS OBISPO BOARD OF SUPERVISORS  
AGENDA ITEM TRANSMITTAL**

|  |                               |   |  |  |
|--|-------------------------------|---|--|--|
| (1) DEPARTMENT<br>Public Works   |                               | (2) MEETING DATE<br>January 10, 2006  | (3) CONTACT/PHONE<br>Joseph Whalen, Resident Engineer<br>(805) 788-2317                                    |  |
| (4) SUBJECT<br>Submittal of a Resolution Authorizing Execution of Notice of Completion for the Construction of Prefumo Canyon Road Paving, Contract No. 300130   |                               |   |  |  |
| (5) SUMMARY OF REQUEST<br>Union Asphalt, Inc. has completed the subject project. It is now necessary that your Board record a Notice of Completion.  |                               |   |  |  |
| (6) RECOMMENDED ACTION<br>That the attached resolution, which authorizes the execution and acceptance of a notice of completion for the Construction of Prefumo Canyon Road Paving, Contract No. 300130, be adopted.   |                               |   |  |  |
| (7) FUNDING SOURCE(S)<br>HES, Road Fund  | (8) PROJECT COST<br>\$564,500 | (9) ANNUAL COST<br>N/A  | (10) BUDGETED?<br><input type="checkbox"/> YES <input type="checkbox"/> N/A<br><input type="checkbox"/> NO |  |
| (11) OTHER AGENCY/ADVISORY GROUP INVOLVEMENT (LIST):<br>Federal Highway Administration and Caltrans  |                               |   |  |  |
| (12) WILL REQUEST REQUIRE ADDITIONAL STAFF? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes, How Many? _____<br><input type="checkbox"/> Permanent _____ <input type="checkbox"/> Limited Term _____ <input type="checkbox"/> Contract _____ <input type="checkbox"/> Temporary Help _____ |                               |   |  |  |
| (13) SUPERVISOR DISTRICT(S)<br>3rd   |                               | (14) LOCATION MAP<br><input checked="" type="checkbox"/> Attached <input type="checkbox"/> N/A  |  |  |
| (15) AGENDA PLACEMENT<br><input checked="" type="checkbox"/> Consent <input type="checkbox"/> Hearing (Time Est. _____)<br><input type="checkbox"/> Presentation <input type="checkbox"/> Board Business (Time Est. _____)   |                               | (16) EXECUTED DOCUMENTS<br><input checked="" type="checkbox"/> Resolutions (Orig + 4 copies) <input type="checkbox"/> Contracts (Orig + 4 copies)<br><input type="checkbox"/> Ordinances (Orig + 4 copies) <input type="checkbox"/> N/A |  |  |
| (17) NEED EXTRA EXECUTED COPIES?<br><input type="checkbox"/> Number: _____ <input type="checkbox"/> Attached <input checked="" type="checkbox"/> N/A   |                               | (18) APPROPRIATION TRANSFER REQUIRED?<br><input type="checkbox"/> Submitted <input type="checkbox"/> 4/5th's Vote Required <input checked="" type="checkbox"/> N/A  |  |  |

Reference: 06JAN10-C-2

C:\Documents and Settings\clanderson.000\Local Settings\Temp\notesFFF692\300130-PREFUMO CNYN-NTC-CVR.wpd.JW:CAH

|   |
|---|
| (19) ADMINISTRATIVE OFFICE REVIEW<br><br>OK Leslie Brown<br><br>B-10<br>(1-10-06) |
|---|



# SAN LUIS OBISPO COUNTY DEPARTMENT OF PUBLIC WORKS

Noel King, Director

---

County Government Center, Room 207 • San Luis Obispo CA 93408 • (805) 781-5252

---

Fax (805) 781-1229

email address: [pwd@co.slo.ca.us](mailto:pwd@co.slo.ca.us)

**TO:** Board of Supervisors

**FROM:** Joseph Whalen, Resident Engineer *JPW*

**VIA:** Glen L. Priddy, Deputy Director of Public Works - Engineering Services *GP*

**DATE:** January 10, 2006

**SUBJECT:** Submittal of a Resolution Authorizing Execution of Notice of Completion for the Construction of Prefumo Canyon Road Paving, Contract No. 300130

## Recommendation

That the attached resolution, which authorizes the execution and acceptance of a notice of completion for Contract No. 300130, be adopted.

## Discussion

This contract provided for paving two sections of Prefumo Canyon Road that were previously gravel in order to improve skid resistance and provide a surface for lane delineation. It is expected that these improvements will reduce the collision rate on the road.

## Other Agency Involvement/Impact

The Federal Highway Administration and Caltrans have provided partial funding for this project under the Hazard Elimination Safety (HES) program.

## Financial Considerations


This multi-year project is included in the current 2005/2006 Fiscal Year Road Budget. The total budget for this project was \$586,500 and the total actual project costs are expected to be \$564,500, for a savings of \$22,000. For a more detailed breakdown of costs and funding, see Exhibit A.

A final report of actual project costs will be filed with the clerk after any and all claims, disputes and adjustments have been resolved. We do not anticipate the final project cost to differ materially from the currently estimated total. Five percent (5%) of total contractor payments are held by the County and released only after meeting the legal holding period after the Notice of Completion is filed.

*B-10  
2*

Funding for the project came from the Federal Hazard Elimination Program (HES) in the amount of \$204,930, and from the Road Fund Capital Projects Division.

The following chart compares the budgeted amount to the current project cost estimate:

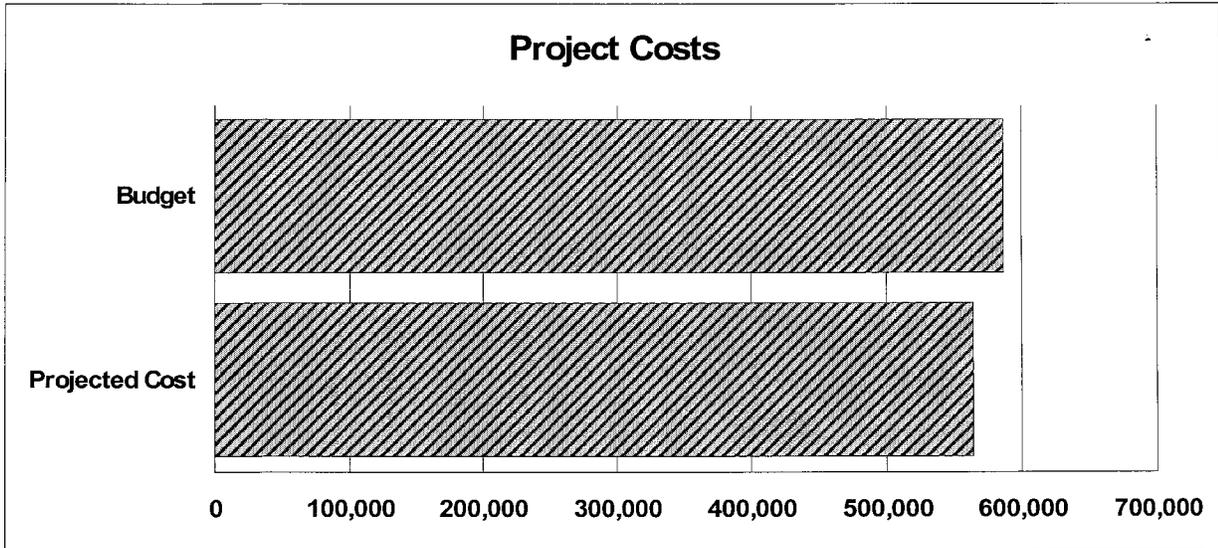

### Results

By taking the recommended action, your Board will cause the legal notice of completion for this construction contract to be recorded, and start the period of time during which liens can be filed by subcontractors against the prime contractor.

Attachments: Vicinity Map  
Exhibit A - Estimated Costs  
Resolution  
Notice of Completion

c: Dave O'Halloran, Construction Engineer

File: Contract No. 300130 - Prefumo Canyon Road Paving

Reference: 06JAN10-C-2


L:\CONSTRUCJAN06\BOS\300130-PREFUMO CANYN-NTC-BLT.wpd.JW:CAH

B-10  
3


# PROJECT LOCATION

**B** P.M. 4.70 to 5.85

**A** P.M. 2.60 to 3.65



NO SCALE

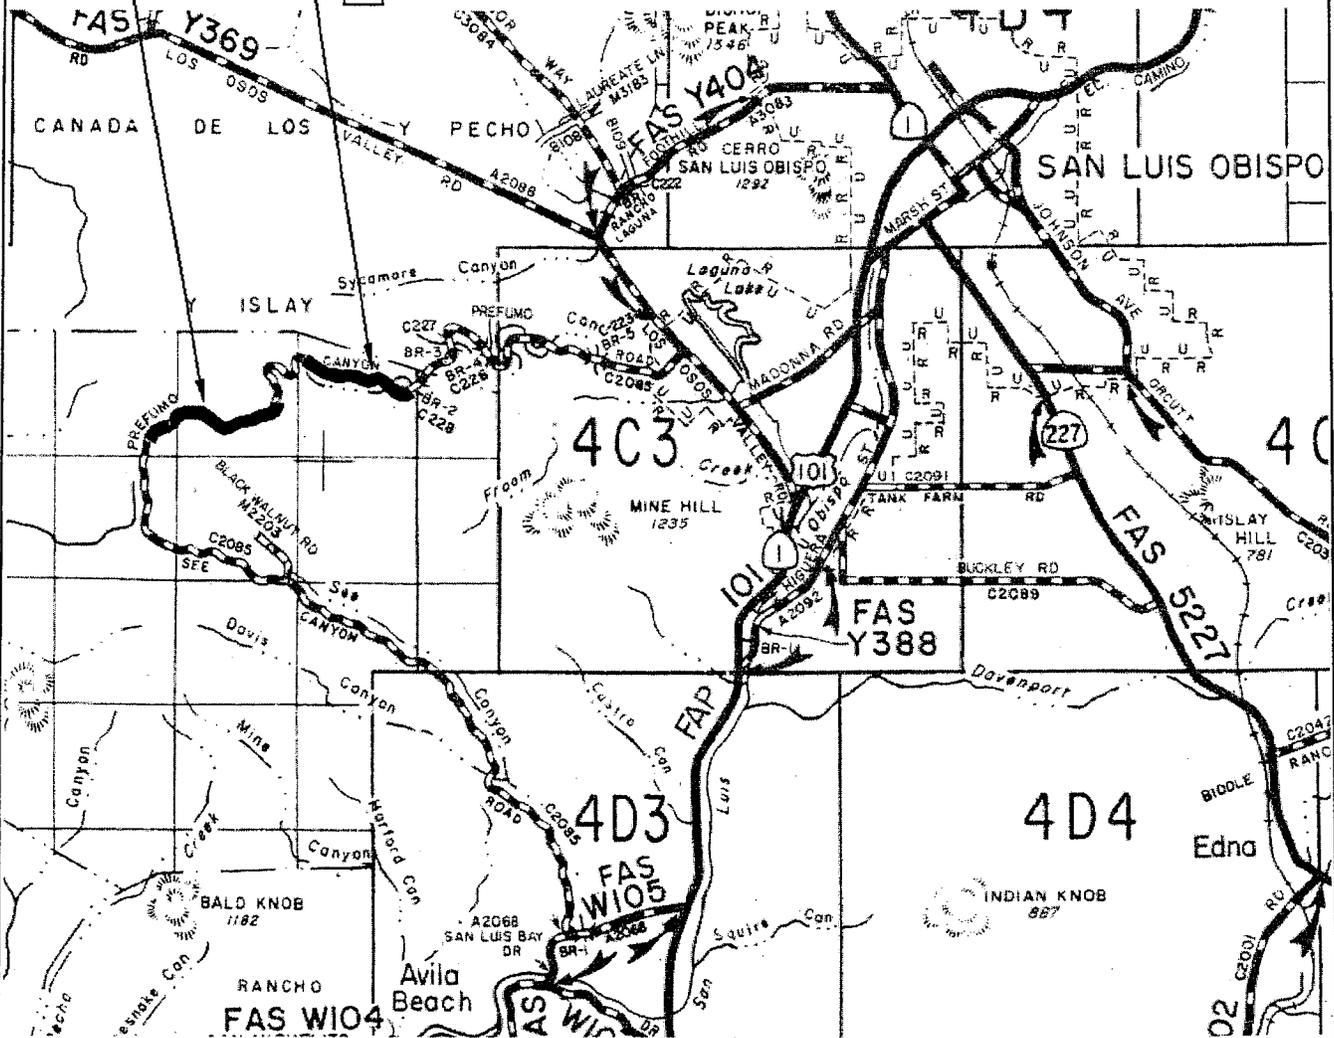

Vicinity Map

W.O. #300130

Co. Rd. No. 2085

PREFUMO CANYON RD PAVING PROJECT  
NEAR SAN LUIS OBISPO, CA.

COUNTY OF SAN LUIS OBISPO PUBLIC WORKS DEPARTMENT

Handwritten signature or initials, possibly "B-10" and "4".

**EXHIBIT A**

Project Cost Estimates

Prefumo Canyon Road Paving Project # P12A158 WBS 300130

| <b>Expenditures:</b>                      | <b>Project Budget</b> | <b>Estimated Project Costs</b> | <b>Variance</b> |
|---|-----------------------|--------------------------------|-----------------|
| Preliminary Engineering                   | 2,300                 | 2,300                          | 0               |
| Environmental Document                    | 10,500                | 10,500                         | 0               |
| Design                                    | 7,600                 | 7,600                          | 0               |
| AD-15 Processing                          | 4,100                 | 4,100                          | 0               |
| Construction*                             | 562,000               | 540,000                        | -\$22,000       |
| Total Expenditures                        | \$586,500             | \$564,500                      | -\$22,000       |
| <b>Budget Funding Sources:</b>            |                       |                                |                 |
| Federal Hazard Elimination Safety Program | 213,300               | 204,930                        | -8,370          |
| Road Fund                                 | 373,200               | 359,570                        | -\$13,630       |
| Total Funding                             | \$586,500             | \$564,500                      | -\$22,000       |

B-16  
5/5

---

**IN THE BOARD OF SUPERVISORS**

County of San Luis Obispo, State of California

\_\_\_\_\_ day \_\_\_\_\_, 20\_\_\_\_

PRESENT: Supervisors

ABSENT:

**RESOLUTION NO.**

**RESOLUTION AUTHORIZING EXECUTION OF NOTICE  
OF COMPLETION AND ACCEPTANCE OF THE  
CONSTRUCTION OF THE PREFUMO CANYON ROAD PAVING  
CONTRACT NO. 300130  
COUNTY OF SAN LUIS OBISPO**

The following resolution is now offered and read:

**WHEREAS**, it appears that Union Asphalt, has fully completed the Construction of Prefumo Canyon Road Paving at San Luis Obispo County, Contract No. 300130; and

**WHEREAS**, it is necessary and desirable that the Notice of Completion and Acceptance be recorded.

**NOW, THEREFORE, BE IT RESOLVED AND ORDERED** by the Board of Supervisors of the County of San Luis Obispo, State of California:

1. That said work is hereby accepted.
2. That the Chairperson of the Board of Supervisors of the County of San Luis Obispo, State of California be, and hereby is, authorized to execute said Notice of Acceptance of Completion.
3. That the Chairperson of said Board be, and hereby is, authorized and directed to record the same.

B-16  
6

Upon motion of Supervisor \_\_\_\_\_, seconded by  
Supervisor \_\_\_\_\_, and on the following roll call vote, to wit:

AYES:

NOES:

ABSENT:

ABSTAINING:

the foregoing Resolution is hereby adopted.

\_\_\_\_\_  
Chairperson of the Board of Supervisors

ATTEST:

\_\_\_\_\_  
Clerk of the Board of Supervisors

[SEAL]

L:\CONSTRUCTION\061805\300130-PREFUMO CNYN-NTC-RESO.wpd.JW:CAH

STATE OF CALIFORNIA, }  
County of San Luis Obispo, } ss.

I, \_\_\_\_\_, County Clerk and ex-officio Clerk  
of the Board of Supervisors, in and for the County of San Luis Obispo, State of California, do hereby  
certify the foregoing to be a full, true and correct copy of an order made by the Board of Supervisors, as  
the same appears spread upon their minute book.

WITNESS my hand and the seal of said Board of Supervisors, affixed this \_\_\_\_\_  
day of \_\_\_\_\_, 20 \_\_\_\_\_.

(SEAL)

\_\_\_\_\_  
County Clerk and Ex-Officio Clerk of the Board  
of Supervisors

By \_\_\_\_\_  
Deputy Clerk

B-14  
7

