



Cayucos Vet's Hall Restoration

Project Update - 07/11/18

1) Project Milestones

02/20/18 - CA Dept of Parks and Recreation completes CEQA process- Notice of Exemption received

03/15/18 - Coastal Development Permit (CDP) application submitted to County Planning

04/26/18 - Received comments back from County Planning regarding remaining items needed to complete the CDP application.

2) Action Items

- Respond to County Planning comments on permit application by 7/25/18.
- Confirm Cal Fire, Cayucos Fire and the CCAC support proposal to convert Ocean Front Ave. to a one-way northbound street into the Vets Hall parking lot. This will allow for the addition of a pedestrian walkway in front of the restored Vets Hall and a loading zone on the opposite side. (Refer attached sketch.)

3) Funding Outlook

- County's 5-Year CIP program
- Prop 68- CA Parks, Environment & Water Bond:
 - o State and Local Parks
 - o Flood Protection
 - o Natural Resource Conservation
- USDA Rural Development Loan
- Local Support and Other Grant Opportunities

4) Project Schedule (Pending Successful Project Funding)

12/01/18 - Coastal Development Permit/County Planning Approval

07/01/19 - Design / Construction Documents Complete


11/01/19 - Building Permit / State & Coastal Commission Approvals

04/01/20 - Approvals / Bidding Process Complete

08/01/21 - Construction Complete

Additional project information can be found at the following web site:

<http://www.slocounty.ca.gov/Departments/Public-Works/Current-Projects/Cayucos-Vets-Hall-Restoration.aspx>

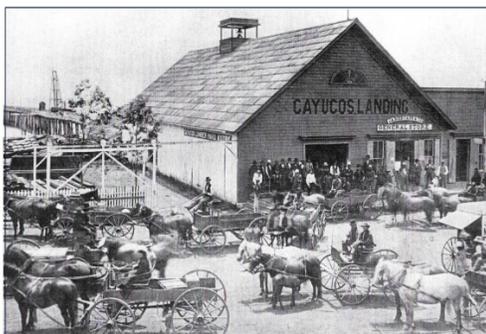

'Butter Day' in Cayucos, circa 1880



Vets Hall Restoration Design- SDG Architects

