



SAN LUIS OBISPO
REGIONAL AIRPORT (SBP)

OUTBOUND BAGGAGE IMPROVEMENTS

July 14, 2026

BIDDING TIMELINE



Bid Advertisement
July 2, 2026



Pre-Bid Conference
July 14, 2026 9:00 AM



Last Day for Questions
July 17, 2026 – 3:00 PM



Bids Due
July 23, 2026 3:00 PM



Bid Opening
July 23, 2026 3:05 PM



Contract Award Within 60 to 90 Calendar Days
Contract time – 180 calendar days



Bid Forms shall be submitted in a sealed envelope and delivered or mailed to the County as indicated in the Notice to Bidders. No electronic bids will be considered.



Site visits may be made available upon request with a minimum two-day notice by contacting airportstaff@co.slo.ca.us or (805) 781-5205

Goals




- Improve baggage screening facility and systems to improve baggage through and bag make-up capacity
- Better ingress egress for personnel
- Process 200 bags/hour
- Minimize impacts to operations
- Provide an enhanced safe work zone

Existing Conditions




- System must remain in operation an hour before flight schedule
- Interim conditions to be installed prior to any demo of existing facilities
- System must be able to process 125 bags/hour
- Utility relocation to be done prior to temporary measures
- Access for luggage carts must be maintained during operating hours.
- Bag belt nighttime hours are 8:00pm – 3:30am*
 - *Departure flight schedules can fluctuate



Existing Conditions

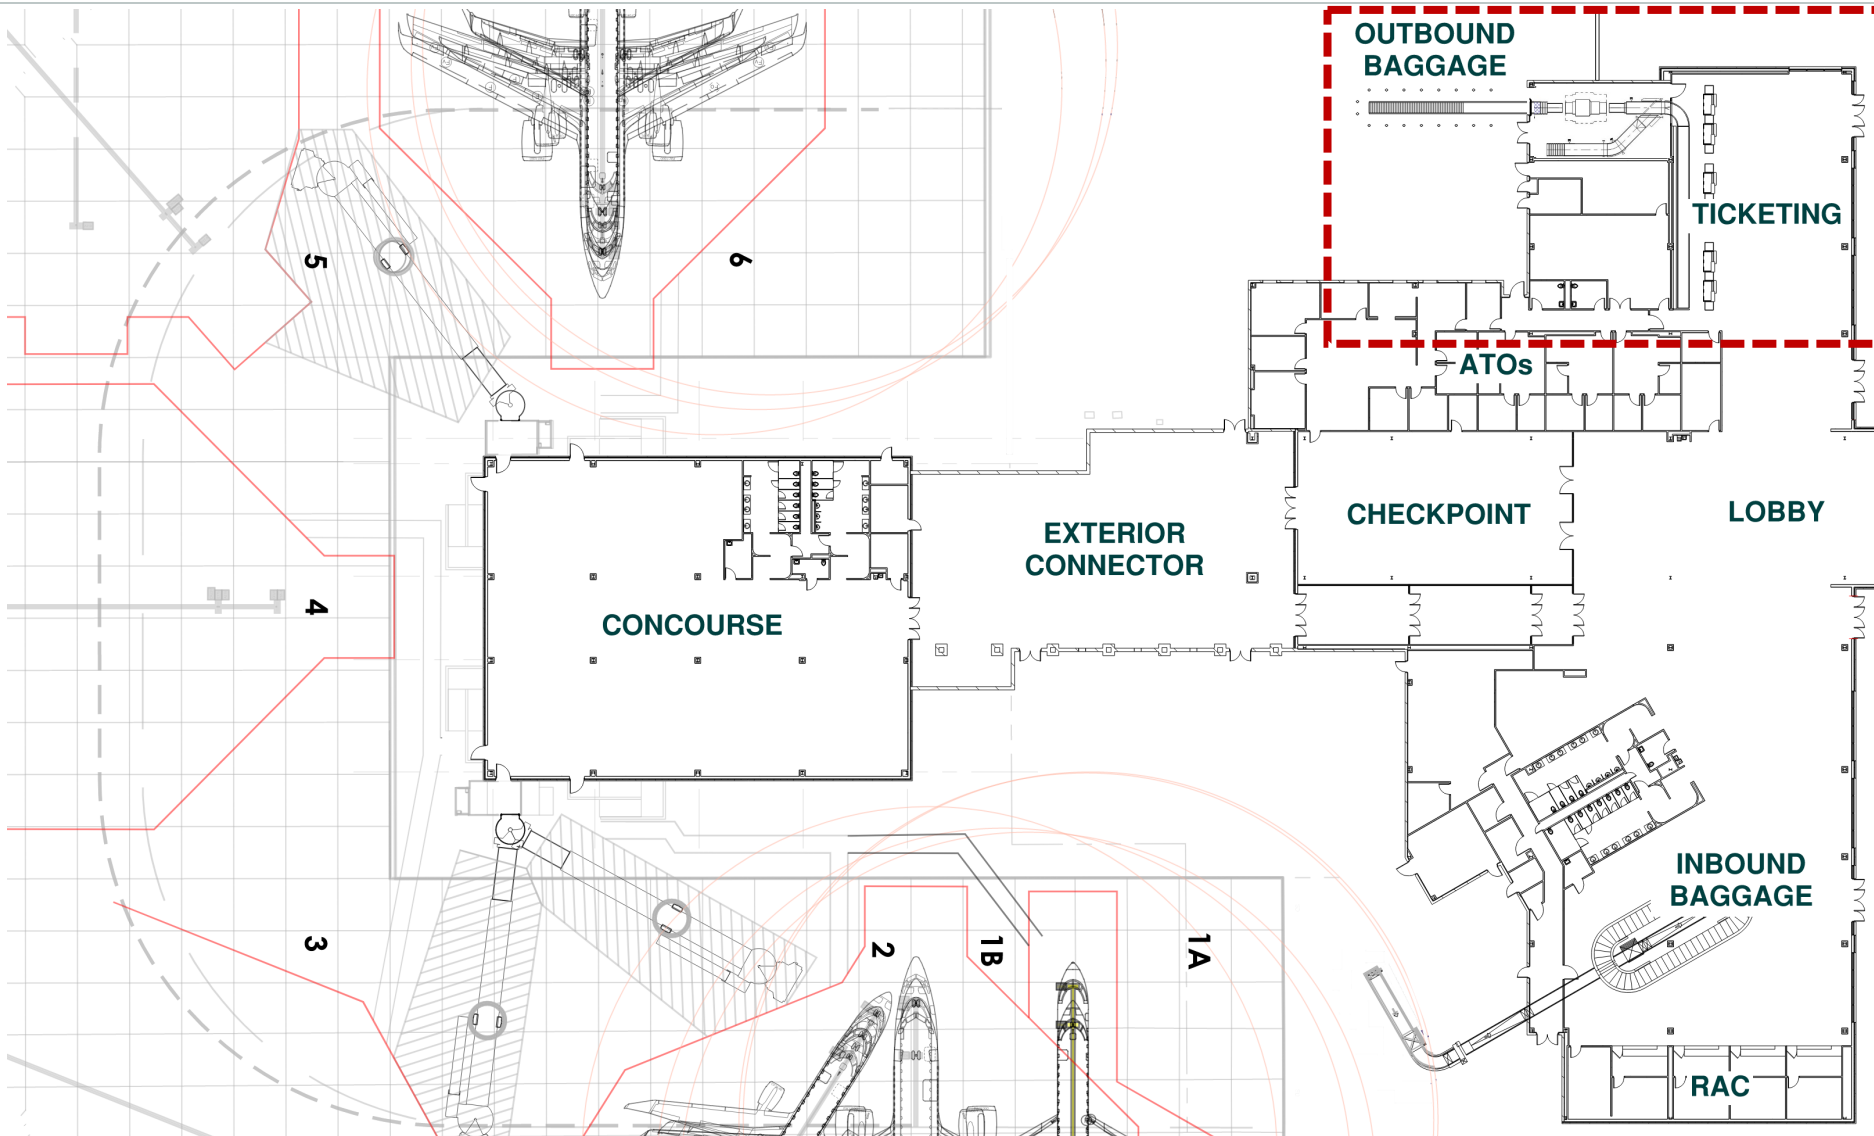

EXISTING CONDITIONS

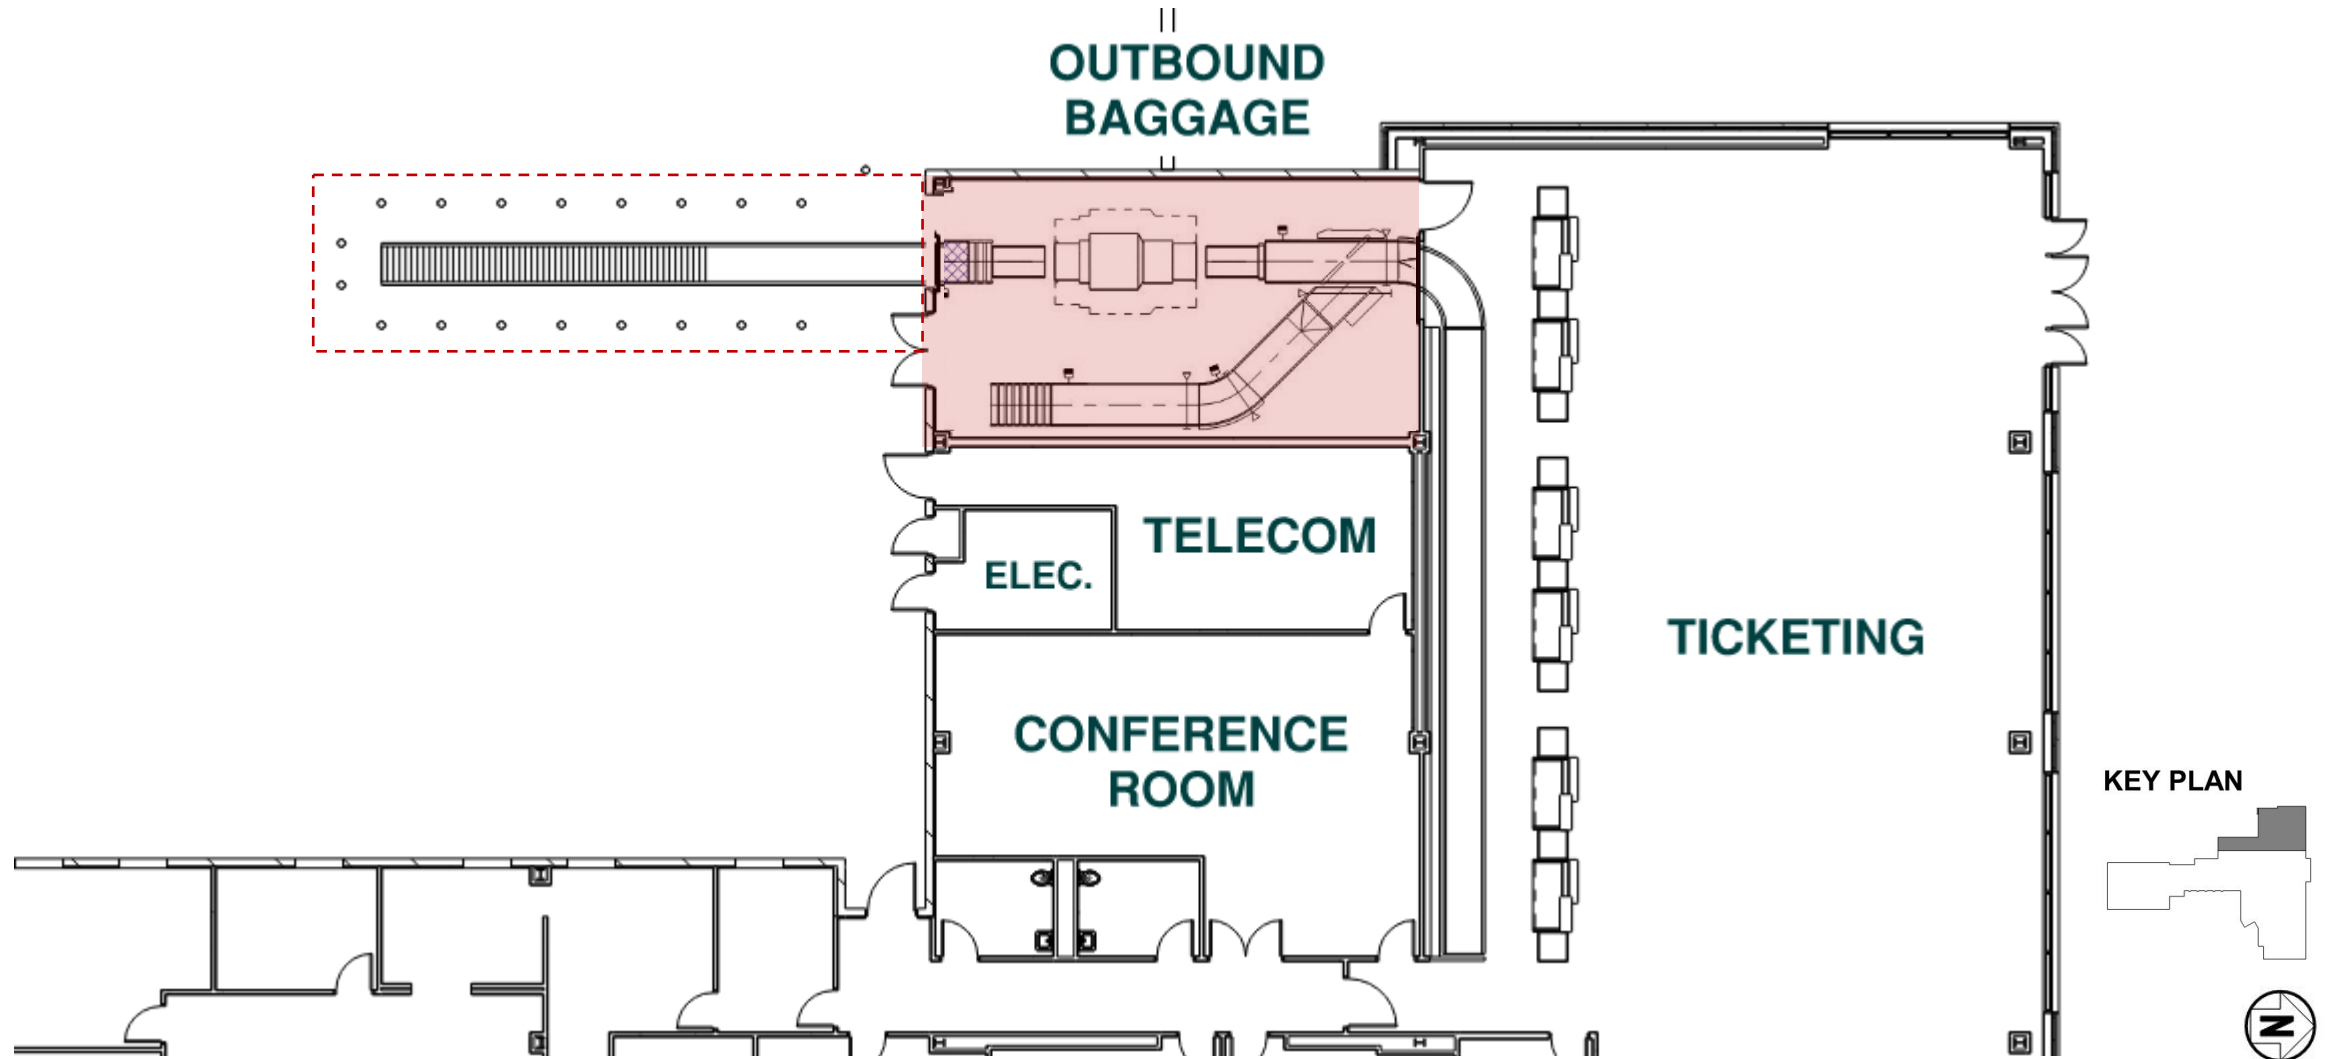

EXISTING CONDITIONS

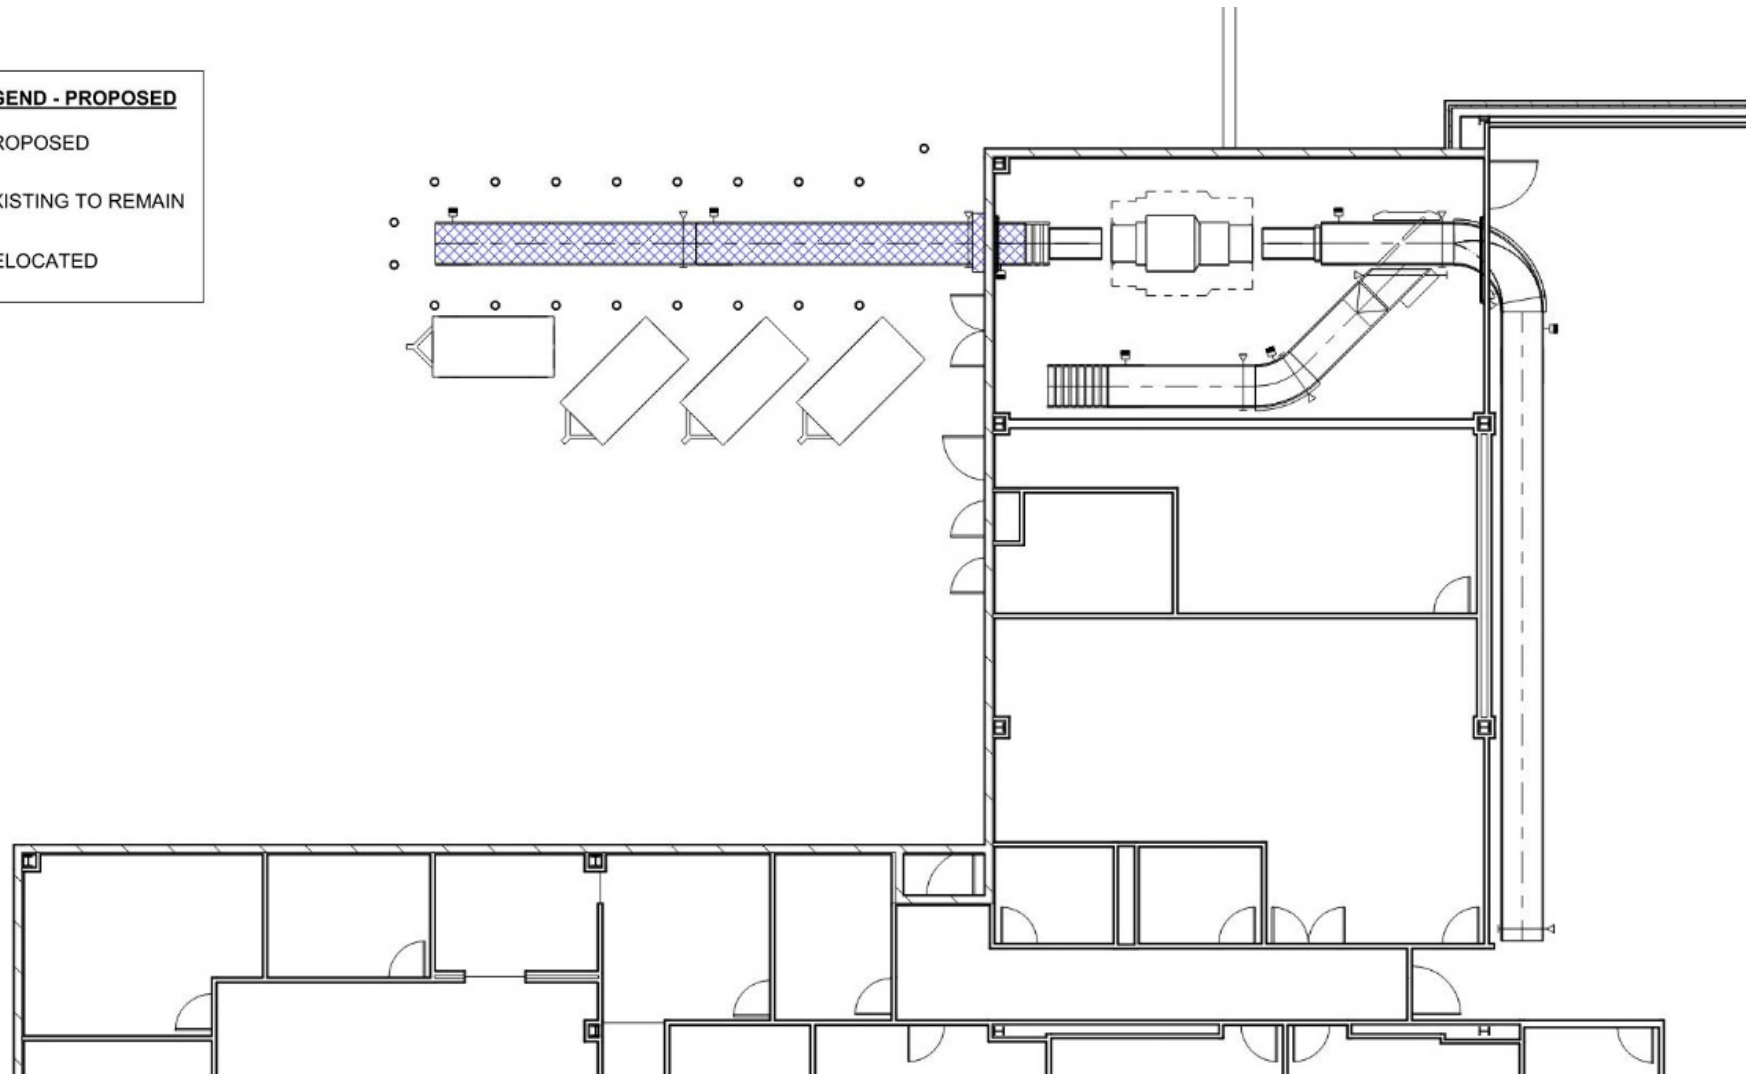


KEY PLAN



A horizontal decorative bar composed of several colored segments: teal, blue, green, light green, dark blue, purple, light blue, olive green, and red.

PROPOSED IMPROVEMENTS


PROPOSED IMPROVEMENTS

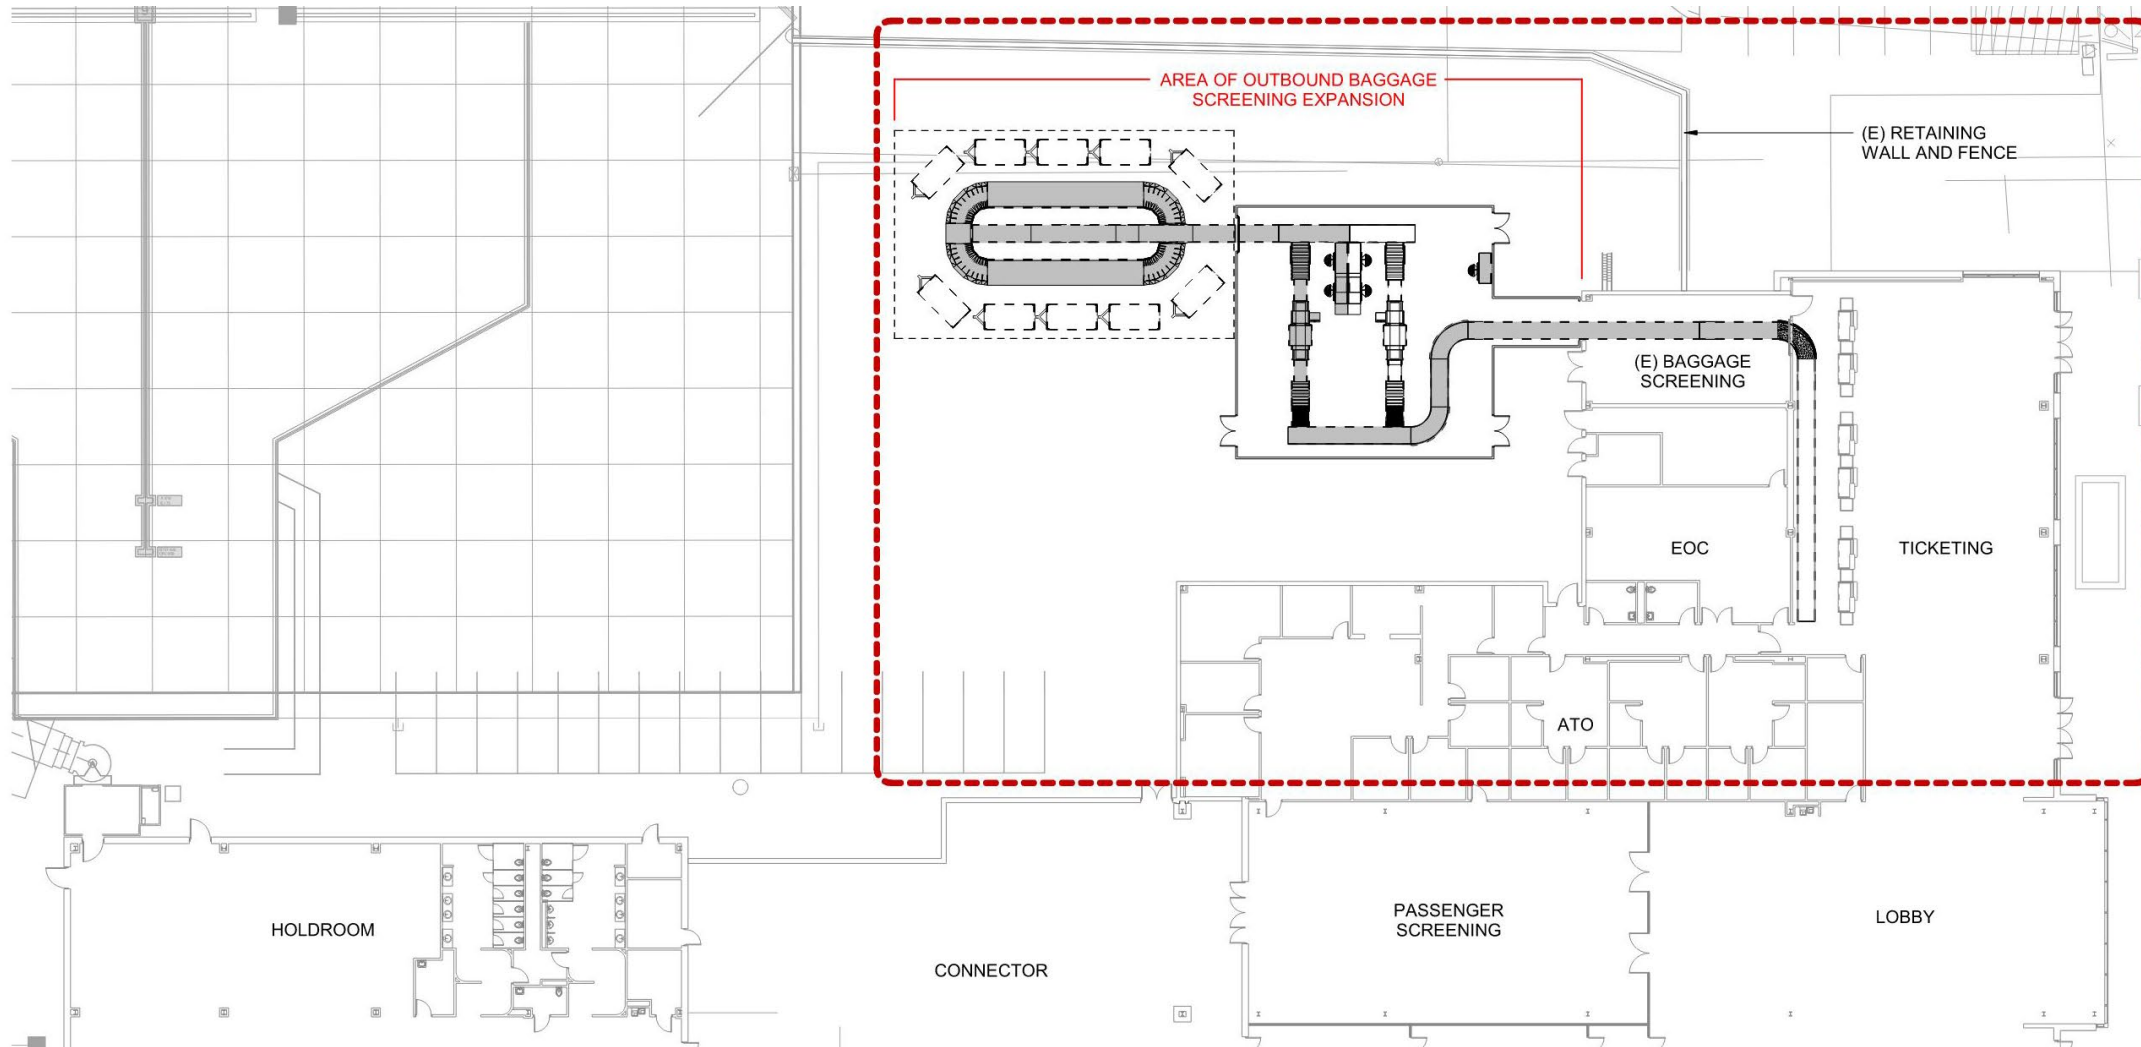


KEY PLAN



PROPOSED IMPROVEMENTS

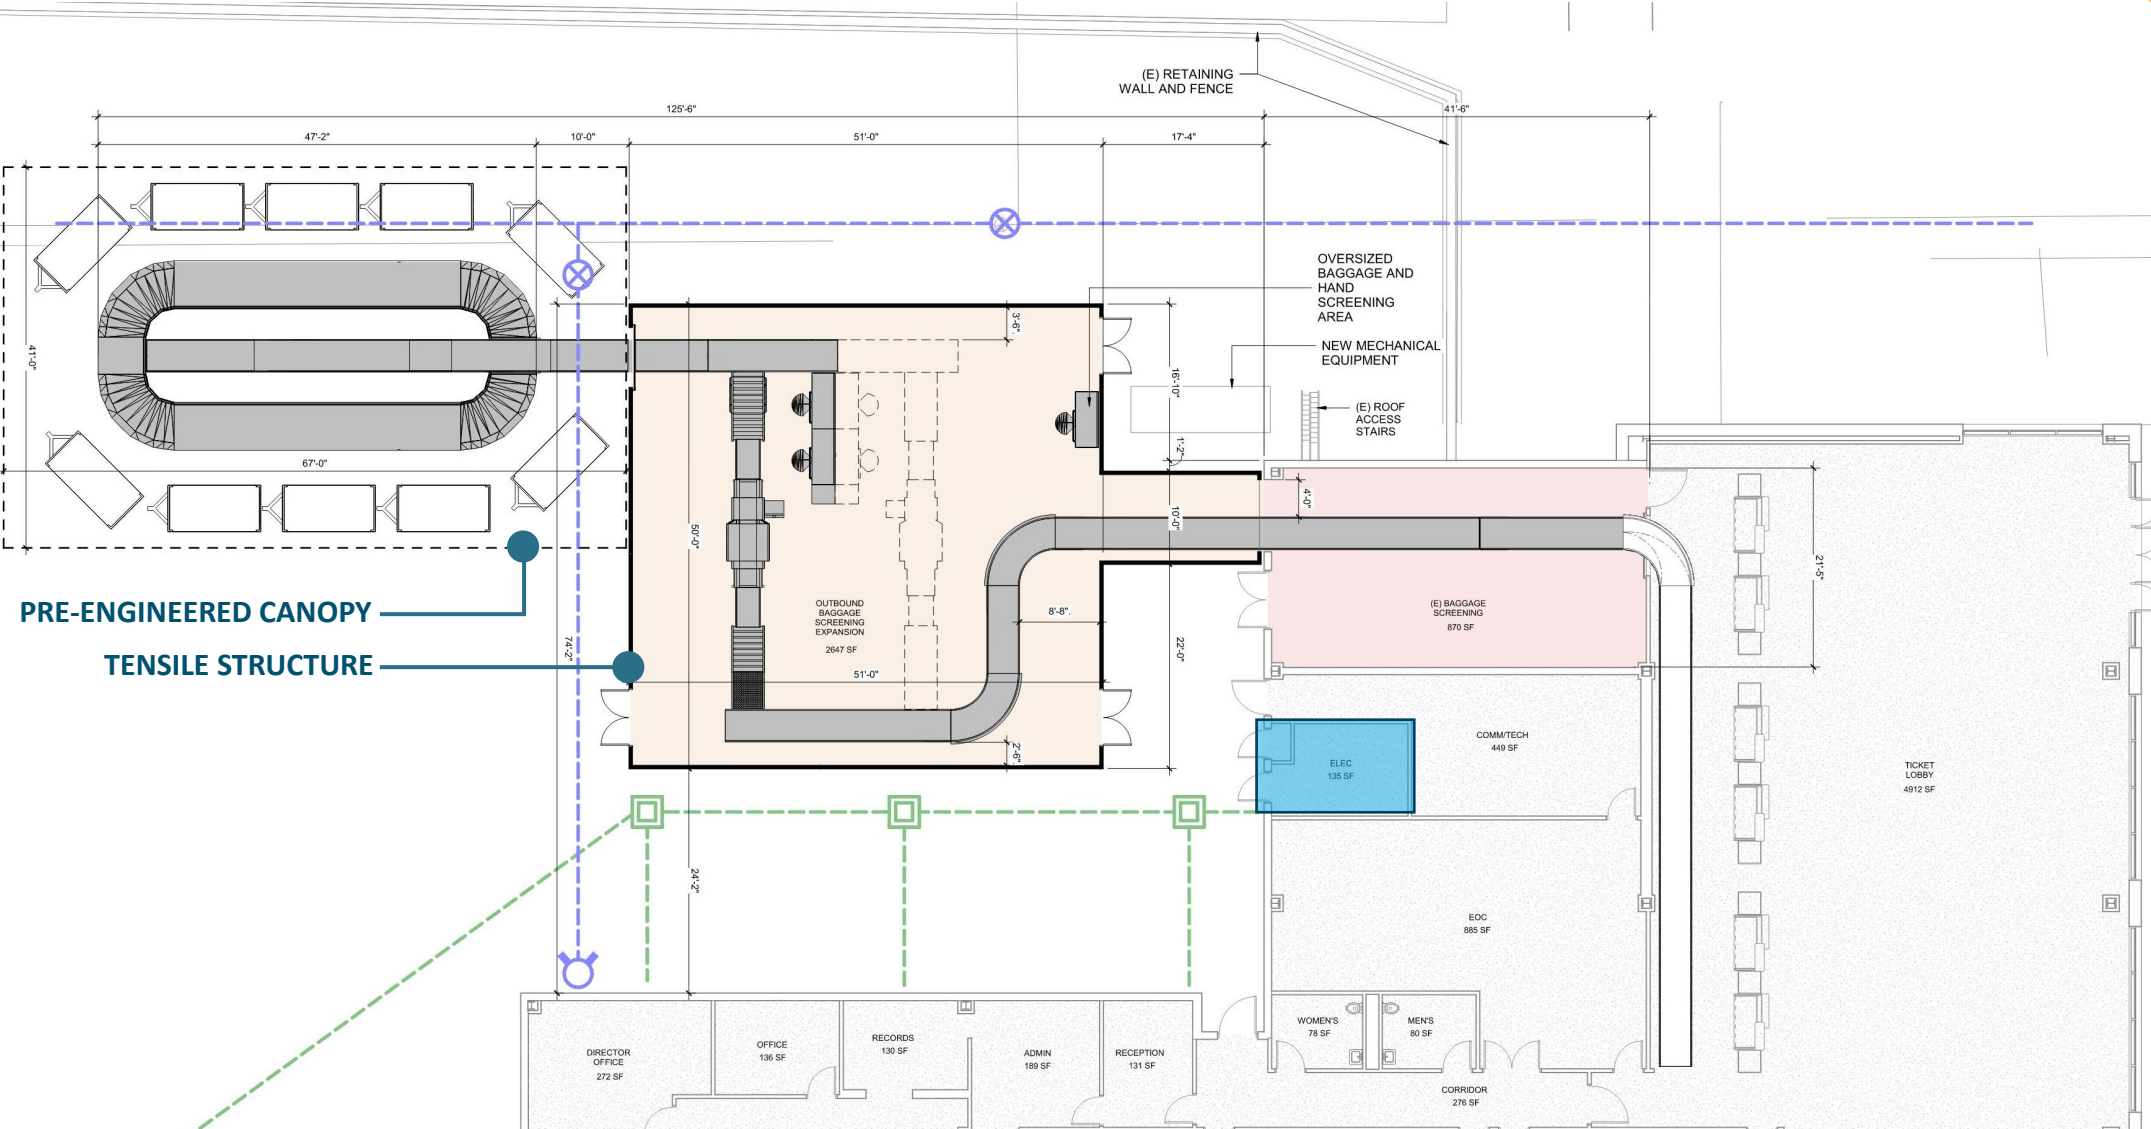

KEY PLAN



PROPOSED IMPROVEMENTS




CANOPY


TENSILE STRUCTURE



PROPOSED IMPROVEMENTS

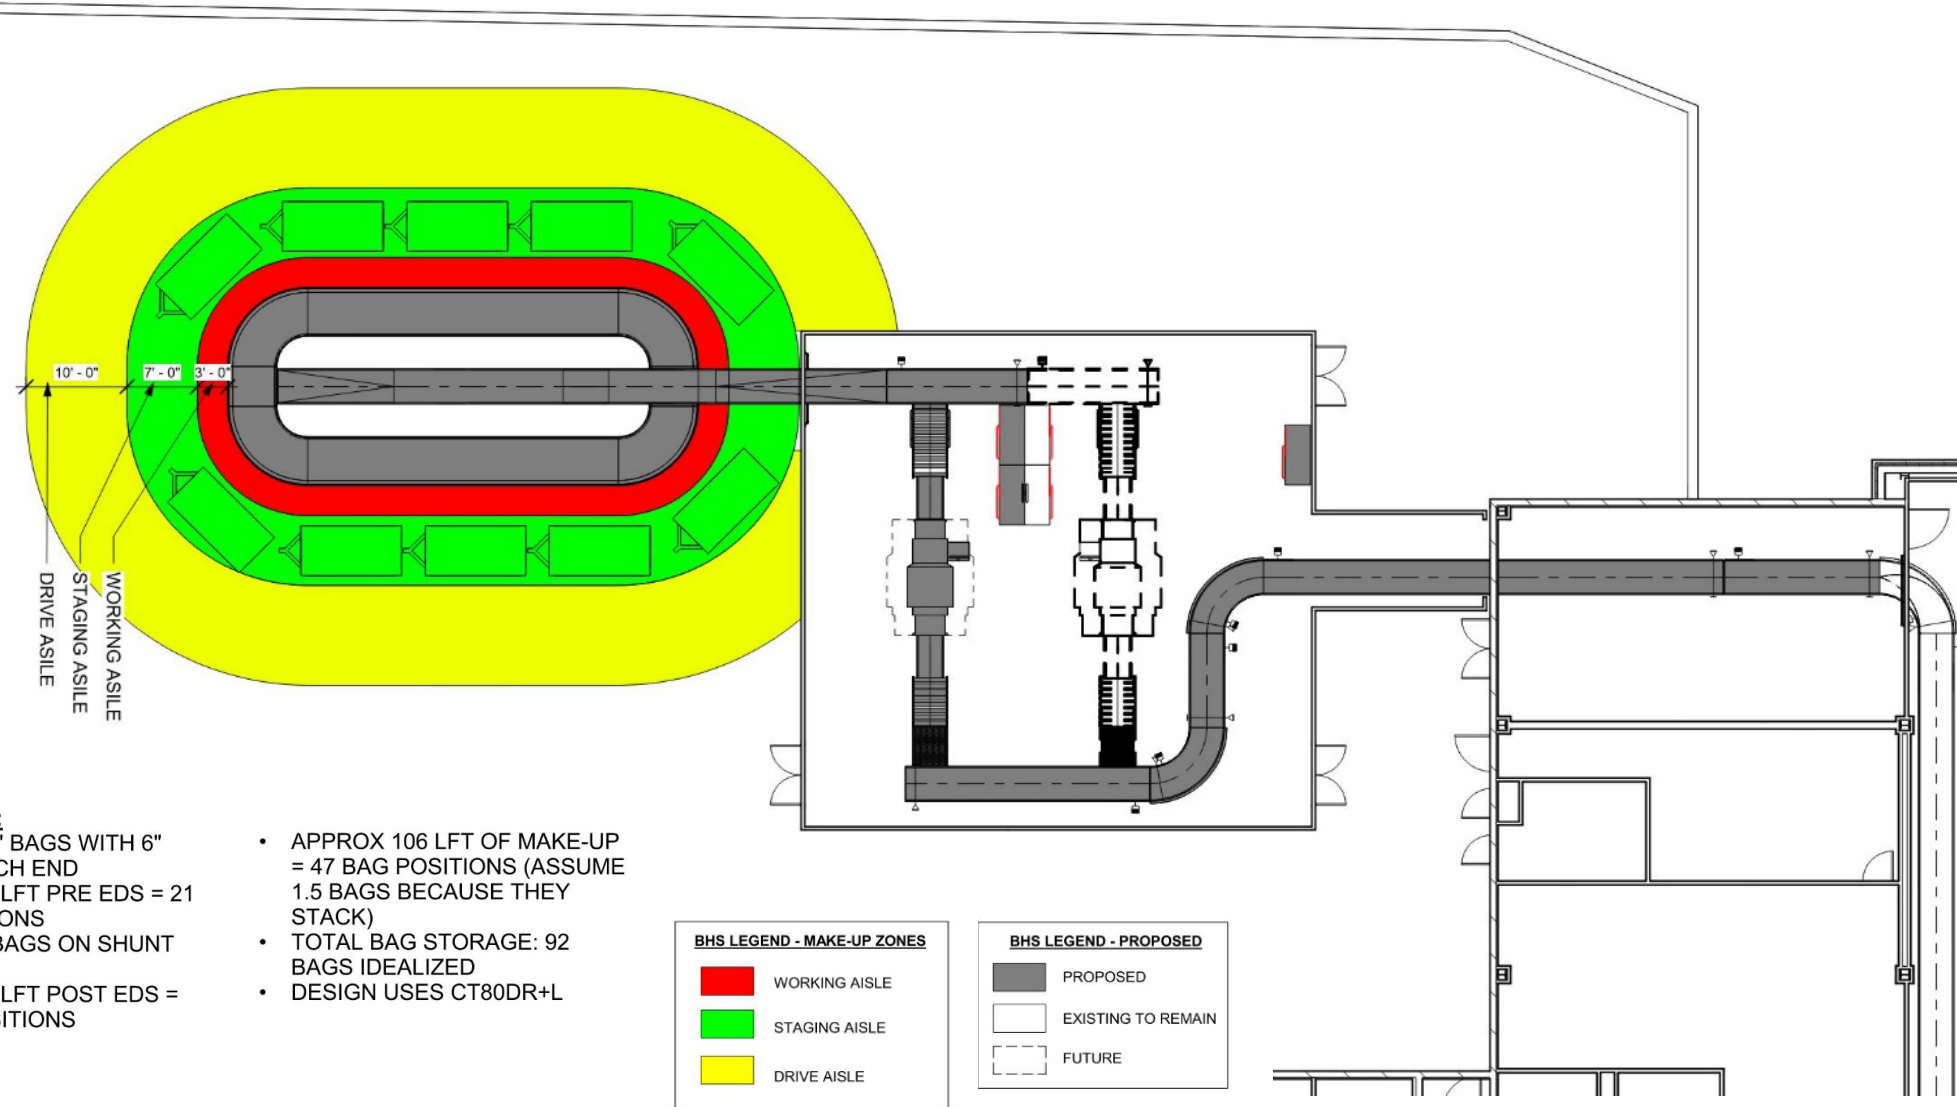

PROPOSED IMPROVEMENTS

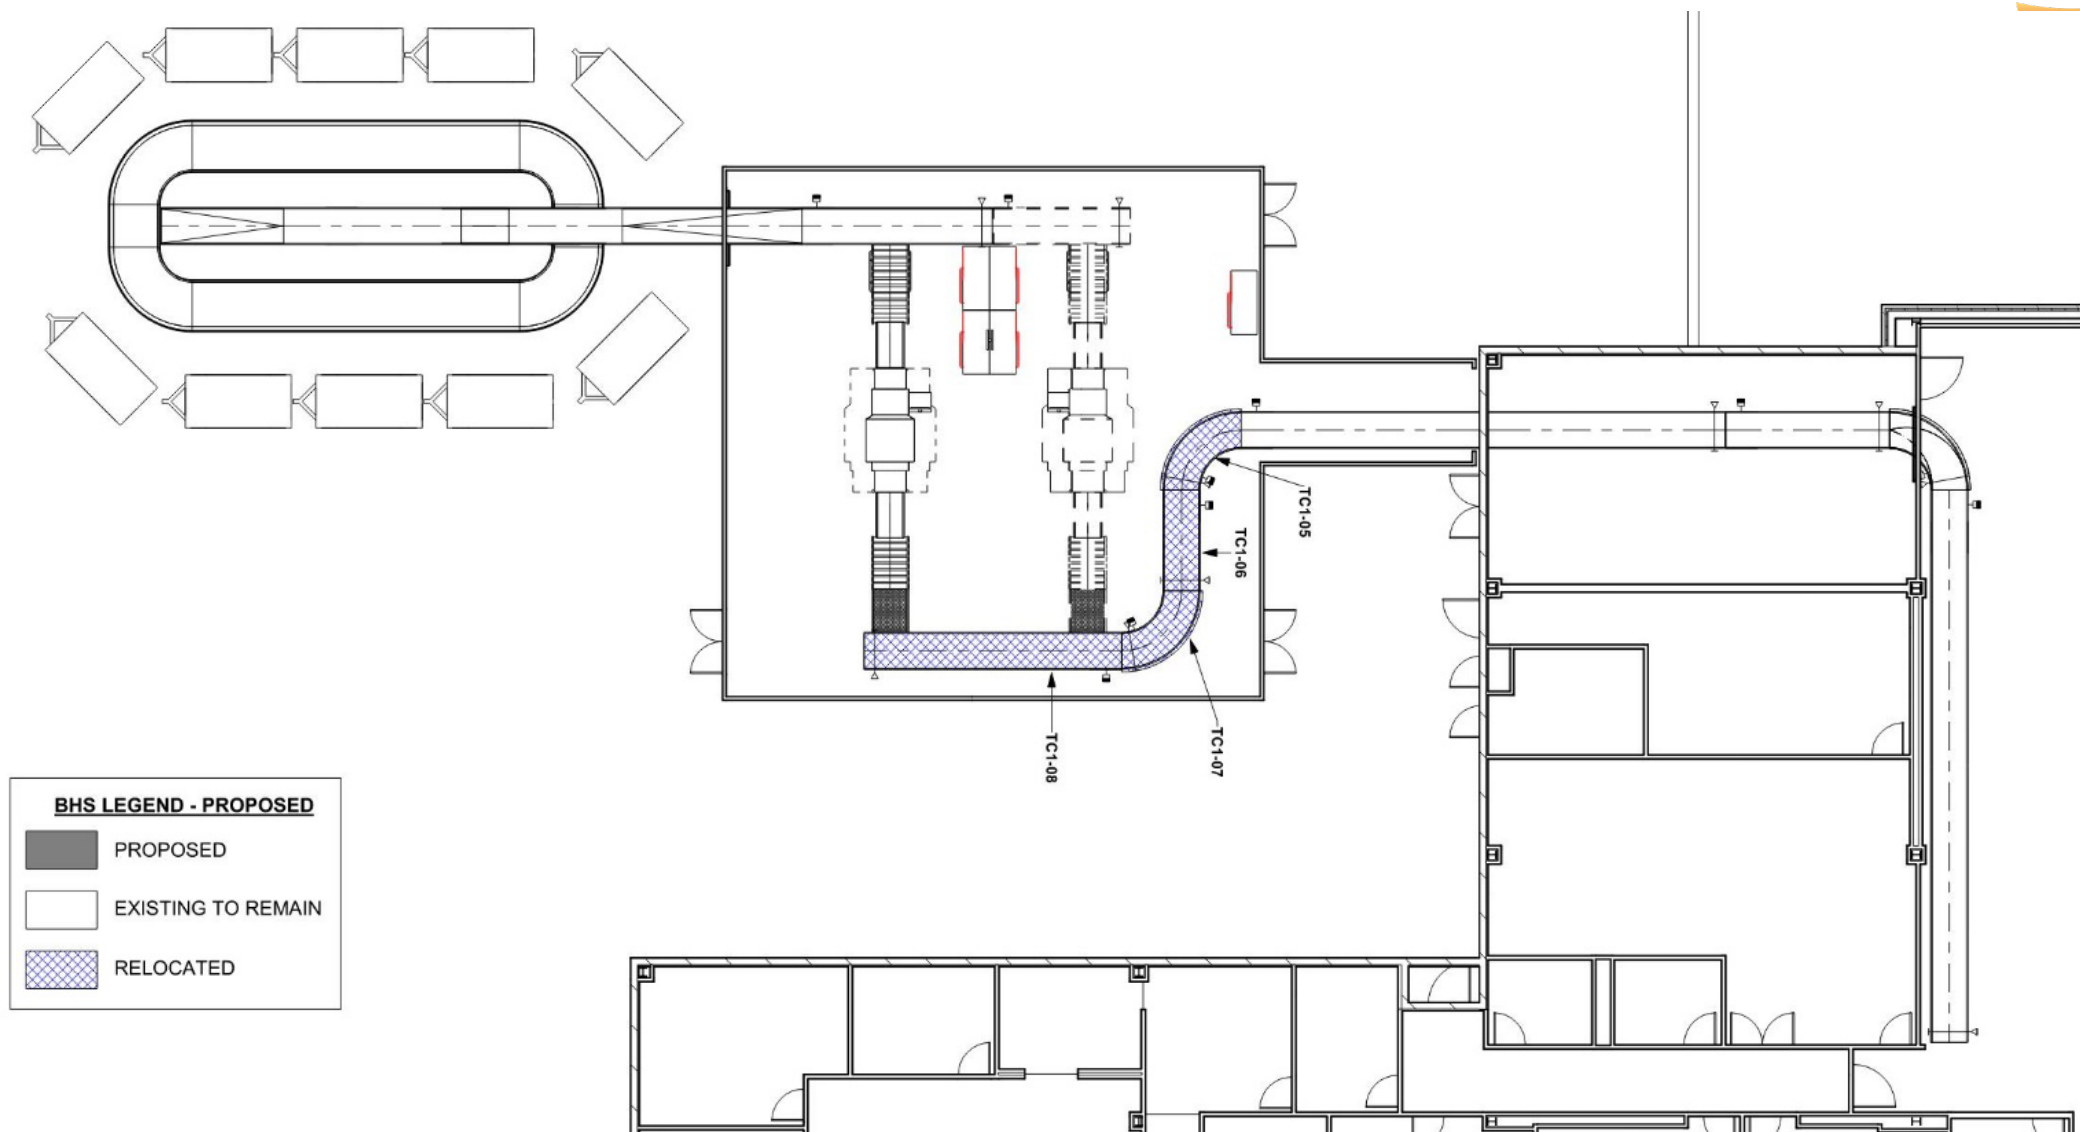


PHASING




BHS LEGEND - PROPOSED

	PROPOSED
	EXISTING TO REMAIN
	RELOCATED

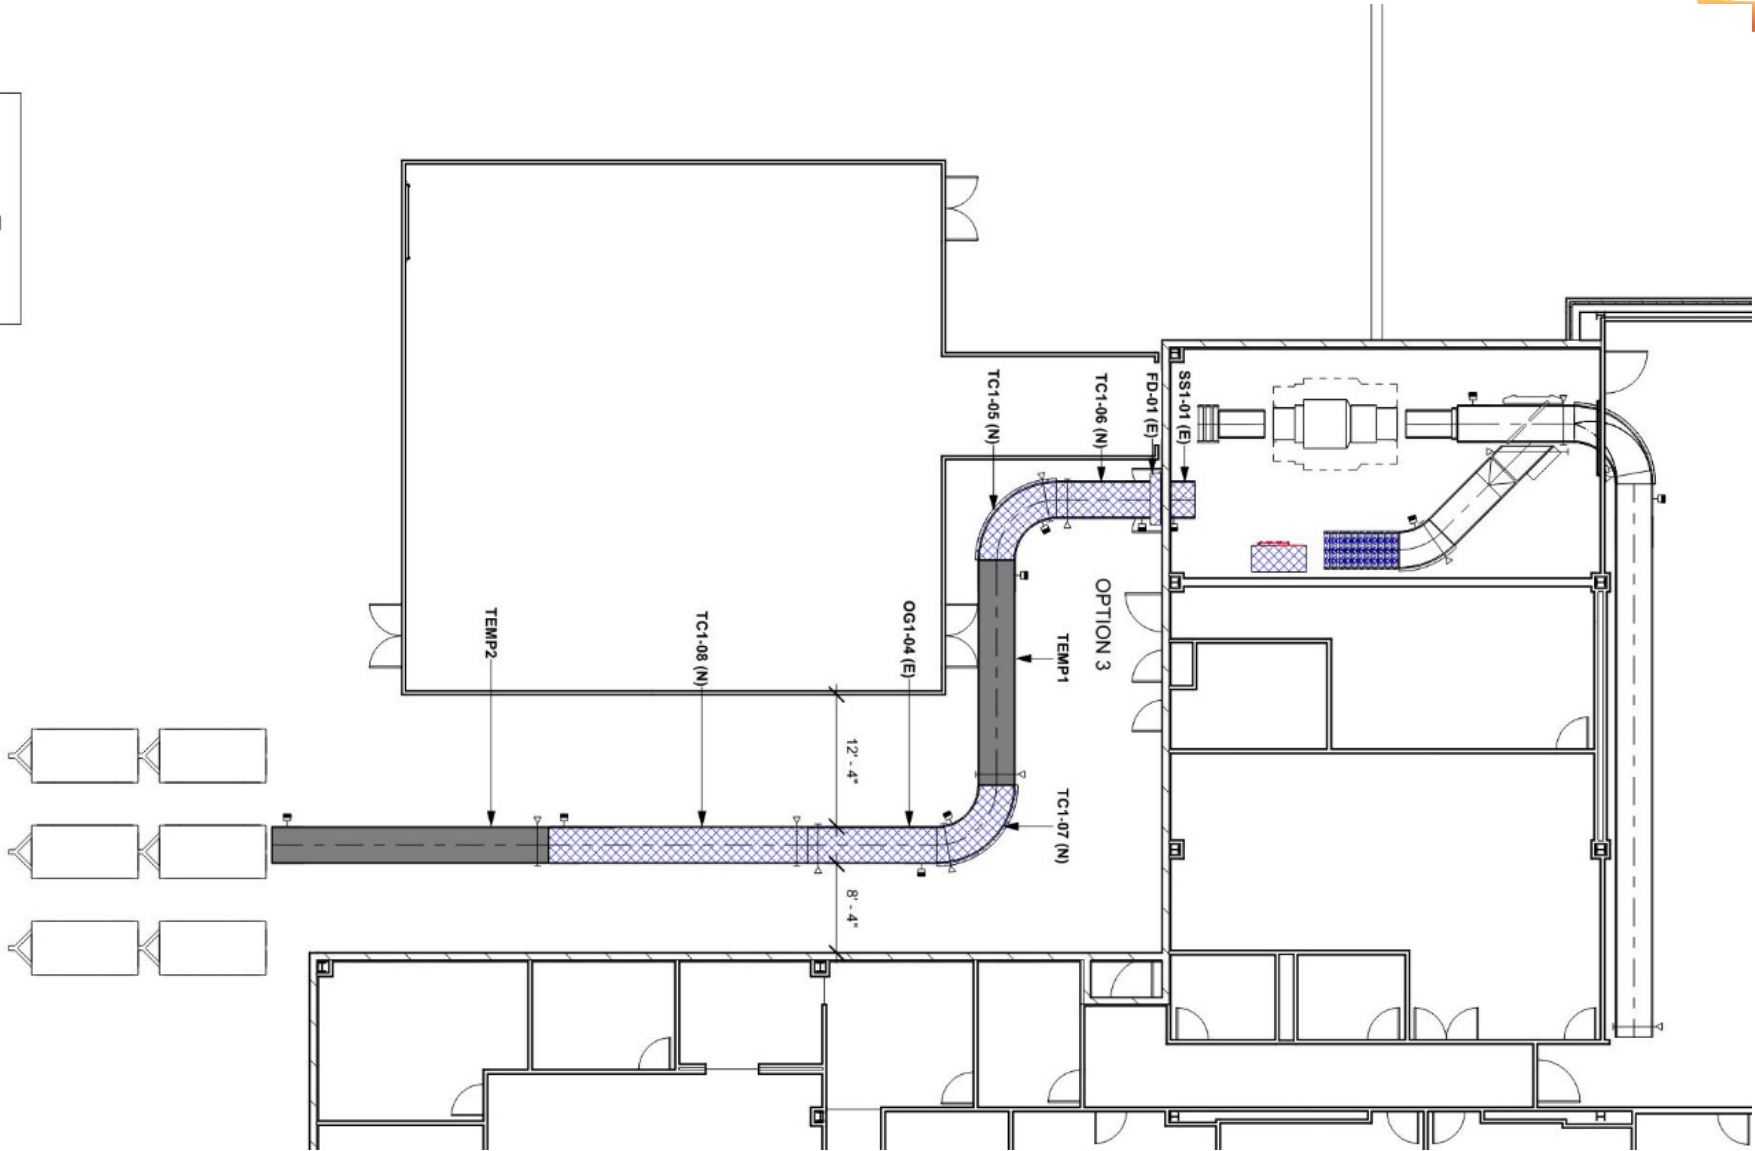


KEY PLAN






- 1 – RELOCATE EXISTING SECURITY DOOR, SECURE OPENING, INSTALL TEMP MAKE-UP AND COVER
- 2 – CONSTRUCT TENSILE TENT STRUCTURE AND CONNECTOR
- 3 – CONSTRUCT CANOPY AT MAKE-UP
- 4 – INSTALL MAKE-UP AND PORTION OF BHS INSIDE STRUCTURE
- 5 – RELOCATE EDS TO TENT STRUCTURE
- 6 – INSTALL REMAINDER OF BHS THROUGH CONNECTOR


KEY PLAN



CONSTRUCTION SITE ACCESS

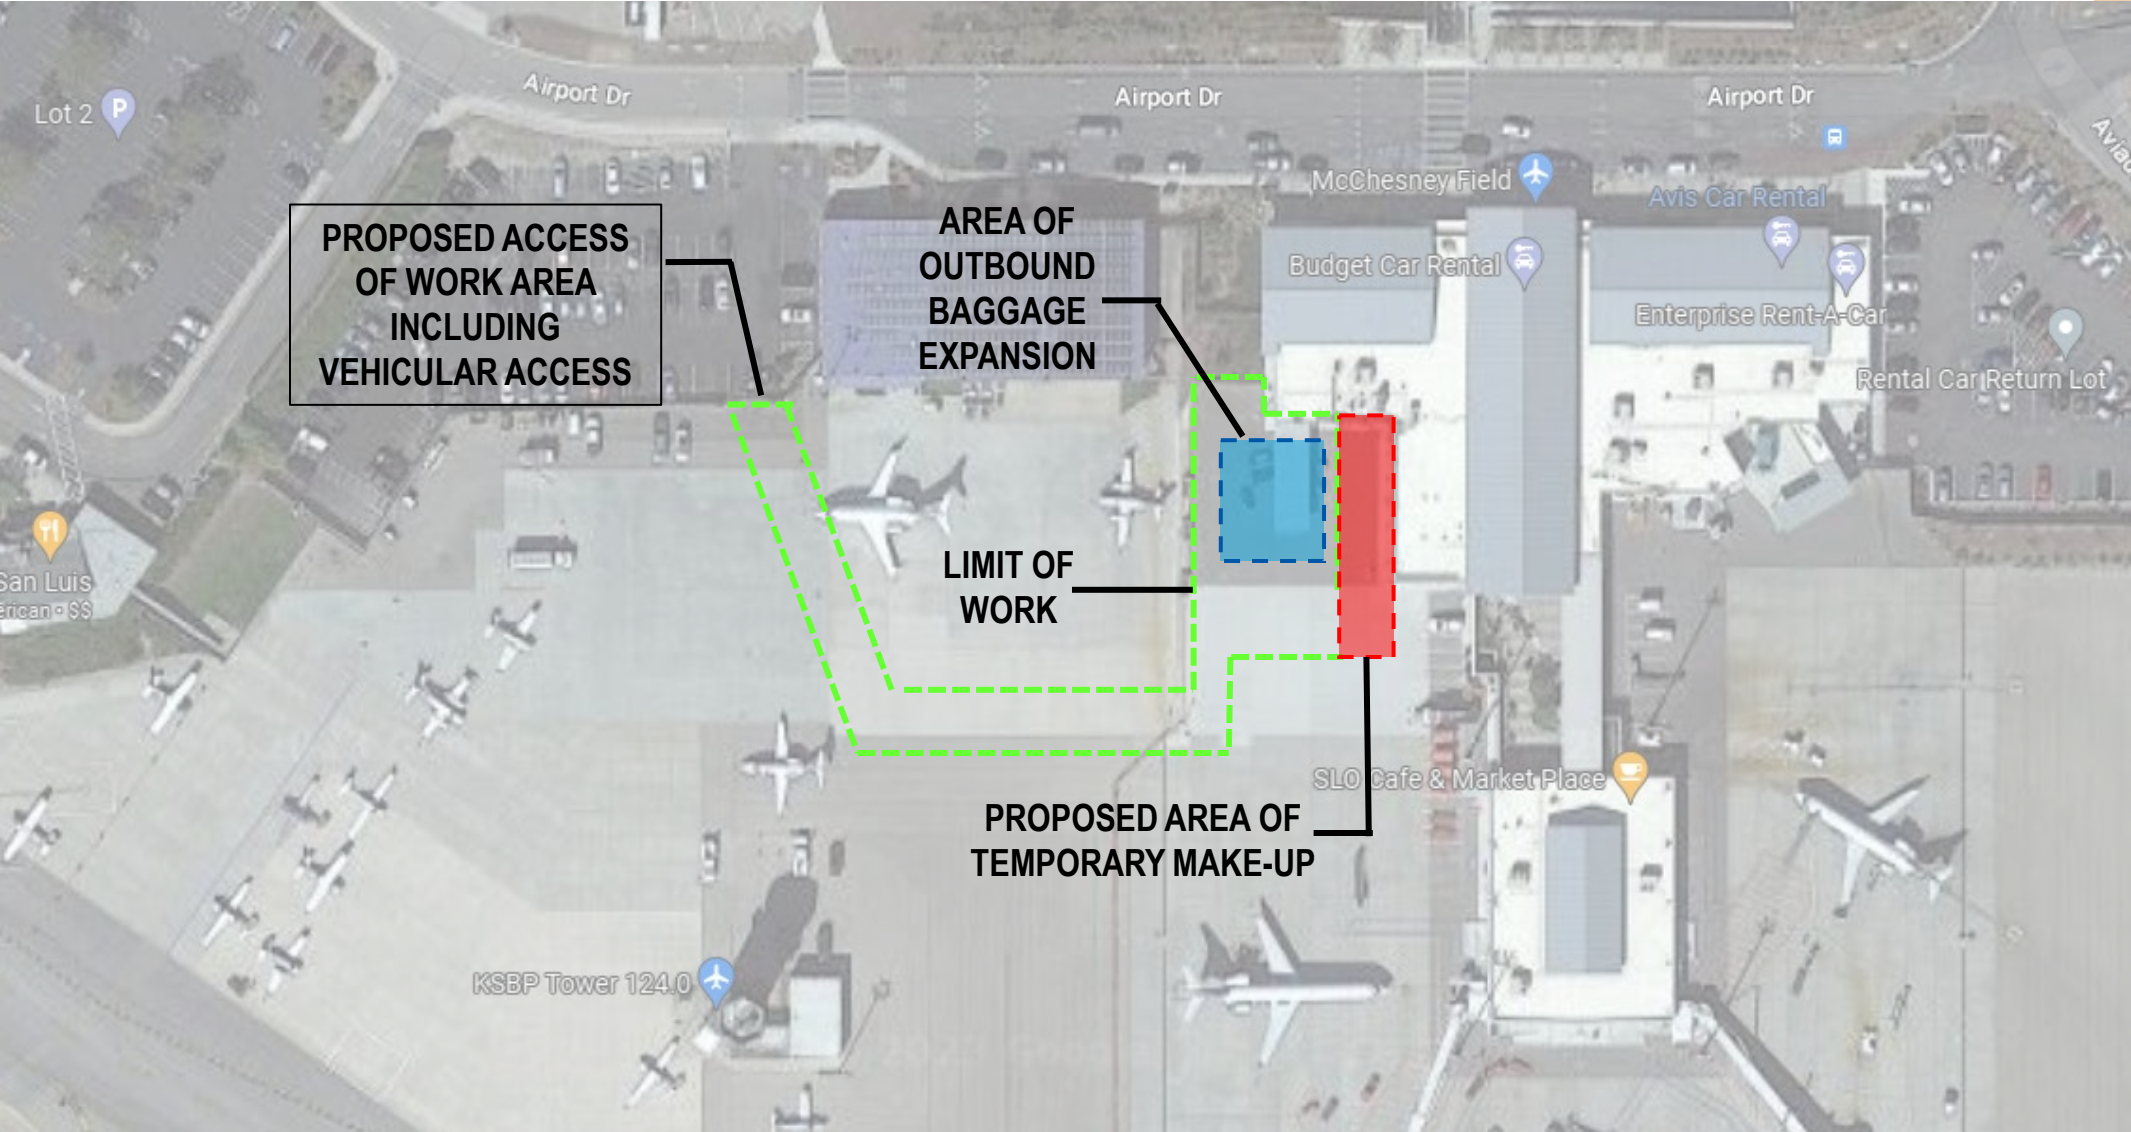

CONSTRUCTION SITE ACCESS

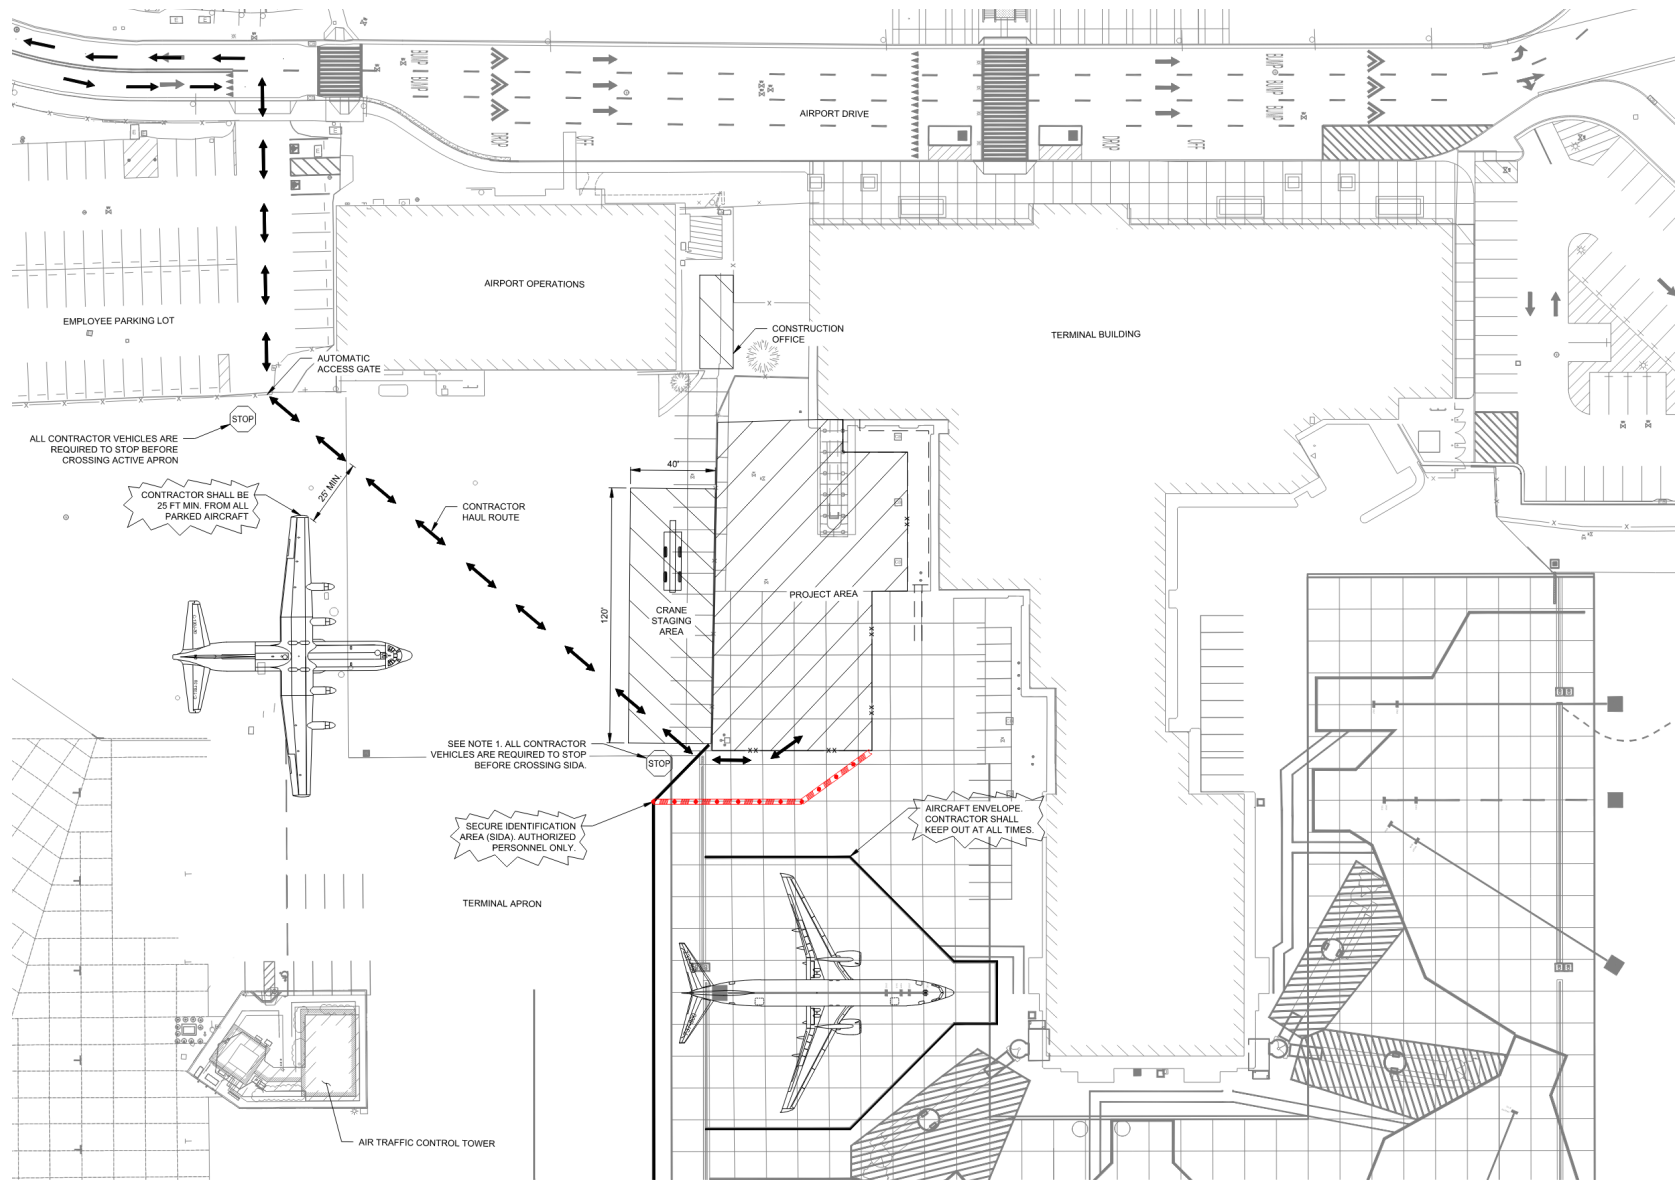

Bid Requirements



- County requirements
- Review and complete Bidder's Checklist
 - Bid schedule – Civil (itemized), Building and equipment (lump sum)
- Federal Contract provisions
 - Certified Payroll Review
- Special Provisions for Airport Construction
 - CSPP
 - Badging
 - Crane clearance – coordination with airport and FAA

Thank you!
